



Acquisition Directorate

Research, Development, Test & Evaluation

FY20 RDT&E Project Portfolio



UNCLAS | FY20 RDT&E Project Portfolio
RDC | A. Arsenault | April 2020



Table of Contents – FY20 RDT&E Project Portfolio

Branch Area	Project #	Project	Slide #
Aviation	5705	Airborne Use of Force (AUF) (Completed)	4
	5601	U.S. Coast Guard Rotary Wing Covert Study	5
	7619 (2020-10)	Autonomous Surface-Search Sensor for Manned Aircraft	6
	7691	Beyond Visual Line of Sight (BVLOS) Technology for Coast Guard (CG) Unmanned Aircraft System (UAS) Operations (Early Start: 2020-12)	7
	7821 (2020-21)	Airborne Counter Unmanned Aircraft Systems (C-UAS)	8
	7820 (2019-35)	Maritime Unmanned System Technology (MUST)	9
C5I (Command, Control, Communications, Computers, Cyber, and Intelligence)	1108	Cell Phone Location for Search and Rescue (Continuation from FY19) (Completed)	10
	1103	Enhanced Person in the Water (PIW) Detection (Completed)	11
	2218	Countering GPS Interference - Legislative Requirement	12
	8116	Intelligence, Surveillance and Reconnaissance (ISR) Enterprise Data Network Study and Analysis - U.S. Department of Homeland Security Science and Technology Directorate funding	13
	8502	Cybersecurity Vulnerabilities, Threats, and Risk Mitigation Strategies for Coast Guard Surface and Air Assets	14
	8120 (2020-5)	Redefine Field Intelligence Reporting and Analysis	15
	7812	Maritime Counter Unmanned Aircraft Systems (C-UAS)	16
E&W (Environment and Waterways)	11011	Performance of Daytime Distress Signals (Continuation from FY19) (Completed)	17
	2702	Develop an Environmentally Friendly Buoy Mooring System (Completed)	18
	4212	Vessel of Opportunity Skimming System (VOSS) Technology Market Research - Oil Spill Liability Trust Fund funding	19
	4705	Oil Sands Products Spill Response - Oil Spill Liability Trust Fund & Great Lakes Restoration Initiative funding	20
	4135 (2020-23)	Ballast Water Management (BWM) Research and Development - Great Lakes Restoration Initiative funding	21
	4711 (2020-17)	Advancing UAS and AUV Capabilities to Characterize Water Column and Surface Oil in Ice Environments - Oil Spill Liability Trust Fund funding	22
	1008	Survival Modeling, Reporting, and Statistics	23
	47041	In-Situ Oil Burn (ISB) Research - Oil Spill Liability Trust Fund & Great Lakes Restoration Initiative funding	24
	1205 (2019-15)	Mass Rescue Life Saving Appliance (MRLSA)	25
	4710	Nearshore and Inland Evaluation of the Estimated Recovery System Potential (ERSP) Calculator - Oil Spill Liability Trust Fund funding	26
	2703 (2020-13)	Next Generation Aids to Navigation Buoys	27



Table of Contents – FY20 RDT&E Project Portfolio

Branch Area	Project #	Project	Slide #
ITNET (IT & Networks)	58041	CG Nearshore Use of FirstNet	28
	7759	Evaluation of Potential CG Use of CubeSats - U.S. Department of Homeland Security Science and Technology Directorate funding	29
	6509	Iceberg Detection and Information Dissemination Methods (Branch Change)	30
	8701 (2019-16)	Automatic Identification System (AIS) Cyber Security	31
	8702 (2020-11)	Evaluate Network Accelerator Technology to Improve Cutter Information Technology (IT) Performance	32
	8503 (2020-24)	Radio Frequency (RF) Communications in a Cloud Environment (NEW)	33
	8107	Extended Reality (XR) Capabilities for Coast Guard Mission Support (Title Change)	34
	8703 (2020-4)	Evaluation and Testing of VHF Data Exchange System (VDES) Impacts on the Automatic Identification System (AIS)	35
MSCOE (Modeling & Simulation Center of Expertise)	3502	Risk Based Cruise Ship Safety Score (Completed)	36
	6512	Ice Condition (ICECON) Risk Assessment Tool(s)	37
	7529	Research into Navigational Safety Risk Modeling and Analysis Tool	38
	7401 (2019-19)	Machine Learning Platforms to Improve Coast Guard Tools	39
	3309	Exploring Machine Learning (ML) for Application in USCG Mission Planning & Disaster Response	40
	9204	Condition-Based Maintenance (CBM) for Coast Guard Asset Product Lines	41
	7937	Incorporating New Sensor Performance in SAROPS	42
Surface	5921	Define and Communicate Exclusion Zones (Continuation from FY19) (Completed)	43
	7758	Evaluation of Three-Dimensional (3D) Printing Technology for Coast Guard Applications (Continuation from FY19) (Completed)	44
	5301	Safety Parameters for ICE Operations (SPICE Ops)	45
	7760	Corrosion Control and Monitoring	46
	62102	Arctic Technology Evaluation 2019-2020	47
	5507	Bromine-Free Water Purification Systems - Legislative Requirement	48
	7210	Low-Cost MDA Pilot - Legislative Requirement	49
	5922	Counter Unmanned Underwater Vehicle (c-UUV)/Anti-Swimmer Technology	50
	5807 (2018-16)	Drug and Explosives Detection Technologies	51



Table of Contents – FY20 RDT&E Project Portfolio

Branch Area	Project #	Project	Slide #
STIC (Science & Technology Innovation Center)	7702	Operational Test Agent (OTA) for the sUAS for NSC Program (Completed) - Procurement, Construction, and Improvement	52
	4110	Diesel Outboard Development (Branch Change)	53
	6812	Support of Alternatives Analysis for the Waterways Commerce Cutter - Procurement, Construction, and Improvement	54
	99953	FY20 Science & Technology Innovation Center Tasks	55
Miscellaneous	N/A	FY20 Short Term Analytical Support Efforts	56



Airborne Use of Force (AUF)

Mission Need: Determine appropriate weapon and ammunition combination to disable non-compliant vessel engines and minimize collateral damage during AUF engagements.

Project Objectives:

- Use computational modeling, limited static and dynamic testing to parameterize secondary effects of various round types when used against representative-sized outboard motors (~75 horsepower and ~200 horsepower) while employing current U.S. Coast Guard (CG) AUF/counter drug techniques, tactics, and procedures.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 18 ✓
Kick-off/Test Design Meeting	28 Nov 18 ✓
Conduct Model Evaluation and Live Fire Test	9 Aug 19 ✓
VIP Demonstration.....	11 Sep 19 ✓
★ Airborne Use of Force (Report)	28 Feb 20 ✓
Project End.....	28 Feb 20 ✓

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date



Sponsor: CG-711
Stakeholder(s): CG-721, ATC Mobile, CG AUF Units, U.S. Army Engineer Research & Development Center

Project #: 5705
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Leverage prior CG Research and Development Center work.
- Collaborate with Federally Funded Research & Development Center or other U.S. Department of Defense partner for live fire range testing.

RDC Research Lead:
Mr. Jay Carey

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

U.S. Coast Guard Rotary Wing Covert Study

Mission Need: Improve covert Tactics, Techniques, and Procedures (TTP) for rotary wing aircraft.

Project Objectives:

- Provide the U.S. Coast Guard (CG) rotary wing aviation community with data that documents the recommended TTPs for conducting covert surveillance.
- Determine lateral and vertical distances for the H-65 and H-60 to remain covert from potential targets in the maritime environment.
- Assist Command, Control, Communications, Computer, Intelligence, Surveillance, and Reconnaissance community with better understanding for future remote sensor acquisitions that allow for well-defined covert standoff distances.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 18 ✓
Define/Limit Target Vessel Parameters.....	17 Dec 18 ✓
Data Collection.....	28 Apr 19 ✓
Aircraft Characteristics Modeling and Simulation.....	30 Aug 19 ✓
Execute Operational Field Test.....	22 Nov 19 ✓
★ Coast Guard Rotary Wing Covert Study (Report & Brief).....	Jun 20
Project End.....	Jun 20

★ Indicates RDC product.




Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

5

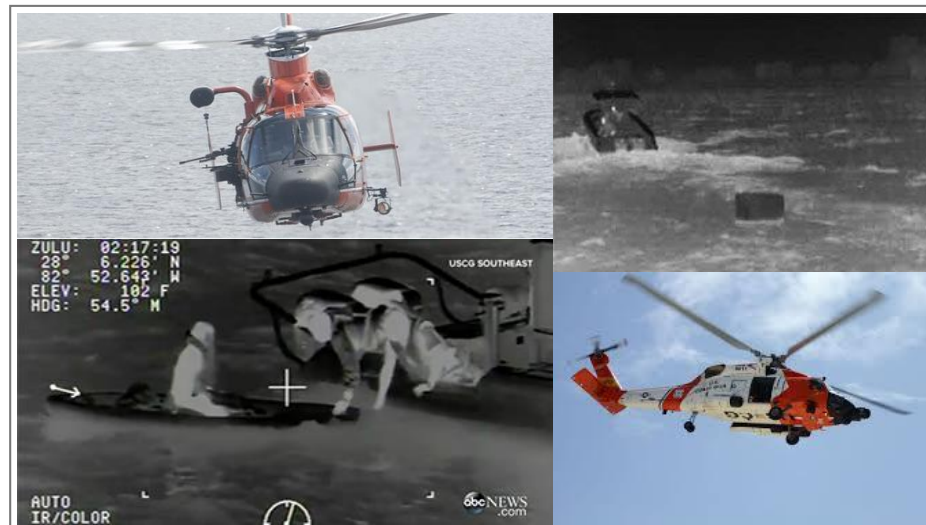

Sponsor: CG-711
Stakeholder(s): CG-SAR, FORCECOM, AREA-3, ALC Vibrations Group

Project #: 5601
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Leverage prior work on CG Research and Development Center Project 8307: Coast Guard Fixed Wing Covert Study.
- KC-130J Aural Detection Information Paper and C-130H Study available as background.

RDC Research Lead:
Ms. Meg Tusia

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Autonomous Surface-Search Sensor for Manned Aircraft

Mission Need: Greater efficiency and effectiveness of searches conducted by airborne assets.

Project Objectives:

- Update research on autonomous sensor systems.
- Determine the potential for autonomous surface-search sensor integration on U.S. Coast Guard (CG) aviation assets.
- Benchmark the use of autonomous surface-search sensors by other agencies.
- Expand the CG's existing autonomous sensor performance data set.
- Model the impact of executing search missions with an autonomous sensor package.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Autonomous Sensor Technology Update.....	1 Feb 20 ✓
Aviation Platform Sensor Integration Analysis.....	Jul 20
Autonomous Surface-search Sensor Benchmarking.....	Jul 20
Mission Performance Modeling.....	Nov 20
★ Autonomous Surface Search Sensor for CG Aviation Assets (Report).....	Apr 21
Project End.....	Apr 21



Sponsor: CG-711

Stakeholder(s): CG-41, CG-SAR, CG-931

Project #: 7619	Anticipated Transition: Knowledge Product Future Technology
------------------------	---

Notes:

- This project builds on autonomous sensor research for unmanned aircraft executed under CG Research and Development Center Project 7810: Advanced Small Unmanned Aircraft System Sensor Investigations.

RDC Research Lead:
Mr. Evan Gross

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Beyond Visual Line of Sight (BVLOS) Technology for Coast Guard (CG) Unmanned Aircraft System (UAS) Operations

Mission Need: BVLOS operations for CG UAS.

Project Objectives:

- Leverage U.S. Southern Command (SOUTHCOM) efforts to explore Vertical Takeoff and Landing (VTOL) operations from a CG Cutter (CGC).
- Establish evaluation team for sense and avoid technologies.
- Submit a Request for Information (RFI) for sense and avoid technologies to assist BVLOS operations.
- Integrate sense and avoid technology for conducting BVLOS operations [sUAS 1st].
- Conduct land and vessel based evaluations using sense and avoid technology [sUAS 1st].
- Incorporate sense and avoid technology into VTOL platform.
- Conduct a VTOL BVLOS Limited User Evaluation from a CGC.
- Inform due regard parameters for CG BVLOS UAS operations.
- Establish a BVLOS Certificate of Authorization for Coast Guard operations.

Key Milestone / Deliverable Schedule:

Project Start.....	13 Mar 19 ✓
Establish Evaluation Team for Sense and Avoid Technologies....	28 Oct 19 ✓
Submit RFI for BVLOS Technologies.....	15 Jan 20 ✓
Coordinate VTOL Demonstrations from a CGC.....	Jul 20
★ VTOL Operations from a CGC (Brief).....	Aug 20
Integrate BVLOS Technologies into sUAS.....	Oct 20
Conduct Land Based BVLOS Tech Demonstration with sUAS.....	Nov 20
Conduct Vessel Based BVLOS Tech Demonstration with sUAS....	Jan 21
★ Land and Vessel Based BVLOS Demonstrations (Brief).....	Feb 21
Integrate BVLOS Tech with VTOL Platform.....	Aug 21
Conduct BVLOS Limited User Evaluation with VTOL.....	Nov 21
★ Beyond Visual Line of Sight UAS Operations (Report).....	Mar 22
Project End.....	Mar 22


★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

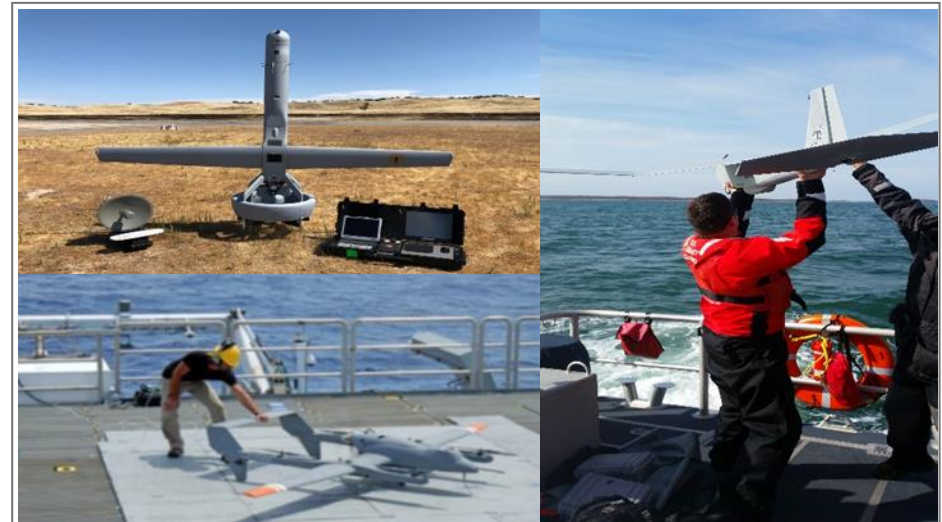

Sponsor: CG-711

Stakeholder(s): CG-751, CG-931, SOUTHCOM, JIATFS

Project #: 7691	Anticipated Transition: Knowledge Product Acquisition Milestone Support
---------------------------	---

Notes:

- Establish Memoranda of Understanding and Cooperative Research and Development Agreements as necessary with industry partners.
- Leverage efforts of SOUTHCOM, Federal Aviation Administration, National Oceanic and Atmospheric Administration (NOAA), Joint Interagency Task Force South (JIATFS), and other government agencies.

RDC Research Lead:
Mr. Stephen Dunn

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Airborne Counter Unmanned Aircraft Systems (C-UAS)

Mission Need: Technology and tactics to secure airspace from small Unmanned Aircraft Systems (sUAS).

Project Objectives:

- Characterize the aviation mission for countering sUAS threats.
- Benchmark ground-based C-UAS solutions and determine the potential for transition to airborne platforms.
- Investigate robust airborne detection, tracking, classification, and identification for airborne assets.
 - Generate a prototype Technical Data Package (TDP) for an airborne C-UAS system.
 - Fabricate and integrate a minimally invasive C-UAS demonstration prototype.
- Conduct prototype test and evaluation to assess functional characteristics.



Key Milestone / Deliverable Schedule:

Project Start.....1 Oct 19 ✓

★ **System Concept (Brief)..... Jul 20**

Airborne C-UAS Limited User Evaluation Sep 21

★ **Airborne C-UAS Technical Data Package (Report).....Apr 22**

Project End.....Apr 22

Sponsor: CG-711

Stakeholder(s): CG-41, CG-711, CG-26, CG-6, CG-5R, ALC

Project #: 7821	Anticipated Transition: Knowledge Product Future Technology
---------------------------	---

Notes:

- This effort will leverage partnerships with the U.S. Department of Homeland Security Science and Technology Directorate, Air Force Research Laboratory, Naval Air Systems Command, and other government organizations.

RDC Research Lead:
Mr. Evan Gross

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Maritime Unmanned System Technology (MUST)

Mission Need: Improved U.S. Coast Guard (CG) persistent maritime domain awareness using Autonomous Underwater and Surface Vehicles (AUSV).

Project Objectives:

- Provided a AUSV platform, study potential employment options for using AUSV to support CG mission areas.
- Explore space, weight, and power requirements.
- Identify possible payloads.
- Conduct single and multiple AUSV evaluations.
- Conduct multiple AUSV swarming evaluations.
- Conduct AUSV and unmanned aerial system teaming evaluations.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Scoping/Baseline and Desired Payload Functional Characteristics.....	Apr 20
Market Research	Jun 20
★ MUST - FY20 Progress Update (Brief).....	Nov 20
Modeling and Simulation Center of Expertise AUSV Sensor Network System Modeling.....	Dec 20
Technical Development/Integration Planning	Jan 21
Test Event 1 – Single AUSV Evaluation	May 21
Test Event 2 – Multiple AUSV Evaluation	Aug 21
★ MUST - FY21 Progress Update (Brief).....	Nov 21
Test Event 3 – Swarming AUSV Evaluation.....	Aug 22
★ MUST - FY22 Progress Update (Brief).....	Nov 22
Test Event 4 – Teaming AUSV Evaluation.....	Sep 23
★ Maritime Unmanned System Technology (Report).....	Nov 23
Project End.....	Nov 23

★ Indicates RDC product.



Sponsor: DHS S&T, CG-261
Stakeholder(s): CG-26, CG-721, CG-MLE

Project #: 7820	Anticipated Transition: Knowledge Product Future Technology
---------------------------	---

Notes:

- Partner with the U.S. Department of Homeland Security (DHS) Science and Technology Directorate (S&T) and U.S. Naval Research Laboratory.

RDC Research Lead:
Mr. Jay Carey

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Cell Phone Location for Search and Rescue

Mission Need: Cell phone technology to support the precise geo-location of distressed mariners in mayday and Search and Rescue (SAR) scenarios.

Project Objectives:

- Conduct market research, identify, and assess state of the market Commercial/Government off the Shelf (COTS/GOTS) geo-locating system(s).
- Evaluate COTS/GOTS solutions on land and at sea to identify possible enterprise solutions.
- Inform functional requirements and Tactics, Techniques and Procedures (TTP) for cell phone geo-location methods.
- Without distracting from the necessity of carrying VHF-FM equipment, contribute to an awareness campaign educating mariners to provide cell phone numbers in float plans, place cell phones in waterproof sleeves, and carry onboard solar cell phone chargers to extend mobile battery life.

Key Milestone / Deliverable Schedule:

Project Start.....	3 Oct 16 ✓
Document Functional Requirements.....	30 Dec 16 ✓
Obtain OTA Agreement with DHS S&T.....	24 Aug 17 ✓
Market Research.....	8 Jan 18 ✓
★ Cell Phone Location for SAR-Market Research (Brief).....	17 Jan 18 ✓
Obtain COTS/GOTS Solutions for Demonstrations.....	14 Sep 18 ✓
Conduct Demonstrations (Lab, Land, and Sea):	
Commercial Solution Pilot Begin SECLI.....	10 Jun 19 ✓
★ Cell Phone Location for SAR (Report)	25 Nov 19 ✓
Project End.....	25 Nov 19 ✓

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

10



Sponsor: CG-SAR
Stakeholder(s): CG-761, CG-BSX, CG-MLE, LANT/PAC-6, C3CEN, C4IT SC, FORCECOM, CBP, DHS S&T

Project #: 1108
Anticipated Transition: Product
Product: Fielded Prototype

Notes:

- Use of Cooperative Research and Development Agreement (CRADA)/S&T Other Transaction Authority (OTA)/S&T Small Business Innovation Research (SBIR).
- Rapid deployment COTS solutions will be investigated in parallel to DHS S&T/CRADA efforts.

RDC Research Lead:
Mr. Sekaran Jambukesan

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Enhanced Person in the Water (PIW) Detection

Mission Need: Maximize the effectiveness of air and surface asset searches for PIW.

Project Objectives:

- Solicit general public through prize competition for modifications/enhancements to floatation devices that increase conspicuity and improve detection probability. Potential benefits include:
 - Increase conspicuity of PIW and small targets in an open water environment using existing U.S. Coast Guard assets.
 - Decrease the time required to search a given open water area in various sea-state and weather conditions.
 - Reduce the burden on air and surface asset sensor operators.
- Perform limited user field evaluations of selected technology.

Key Milestone / Deliverable Schedule:

Project Start.....	2 Oct 17 ✓
Prize Challenge Posting Completed.....	5 Sep 18 ✓
★ Enhanced Person in the Water: Ready For Rescue Prize Challenge Competition (Report).....	20 Dec 18 ✓
RDC Piranha Pool Completed.....	29 Mar 19 ✓
Limited User Evaluation Completed.....	24 Sep 19 ✓
★ Enhanced Person in the Water Detection (Report).....	24 Feb 20 ✓
Project End.....	24 Feb 20 ✓

★ Indicates RDC product.




Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

11

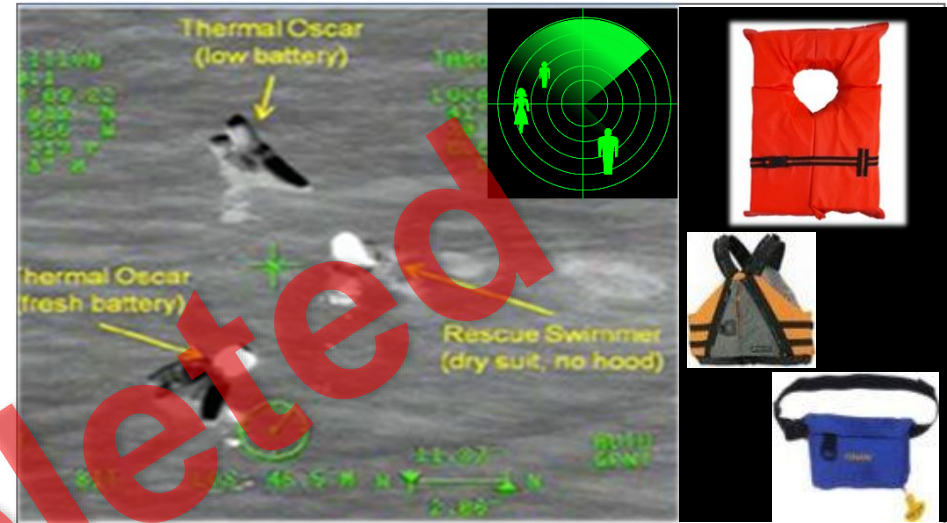

Sponsor: CG-ENG-4
Stakeholder(s): CG-731, CG-411, CG-SAR, CG-761, ATC, CG-BSX, CG-INV, CG-CVC

Project #: 1103
Anticipated Transition: Product
Fielded Prototype

Notes:

- Project includes use of the U.S. Department of Homeland Security Science and Technology Directorate Prize Competition process.

RDC Research Lead:
Ms. Judi Connelly

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Countering GPS Interference

Mission Need: Develop a means to detect, localize, alert, and mitigate sources of Global Positioning System (GPS) interference in the maritime domain.

Project Objectives:

- Develop wide area GPS interference detection based on existing networks of GPS receivers such as Nationwide Automatic Identification System.
- Investigate GPS interference mitigation technologies to counter effects aboard U.S. Coast Guard (CG) vessels. Investigate tactical GPS interference detection capability for CG units to operate to find GPS interference sources.
- Develop notification methods for maritime users via marine safety information methods such as broadcast notice to mariners, Automatic Identification System application specific messages, and navigation data.
- Bring maritime experience to the U.S. Department of Homeland Security (DHS) Science and Technology Directorate (S&T) First Responders & Detection Division (FRD) Position, Navigation and Timing (PNT) efforts.


Key Milestone / Deliverable Schedule:

Project Start.....	14 Jun 18 ✓
DHS S&T 2018 GPS Equipment Tests	21 Sep 18 ✓
Test CG GPS Units at Live Sky Test Event.....	15 Aug 19 ✓
Demonstration of Wide Area GPS Interference Detection.....	26 Sep 19 ✓
★ Countering GPS Interference (Brief).....	7 Oct 19 ✓
★ Countering GPS Interference (Report & Brief).....	Apr 20
Project End.....	Apr 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

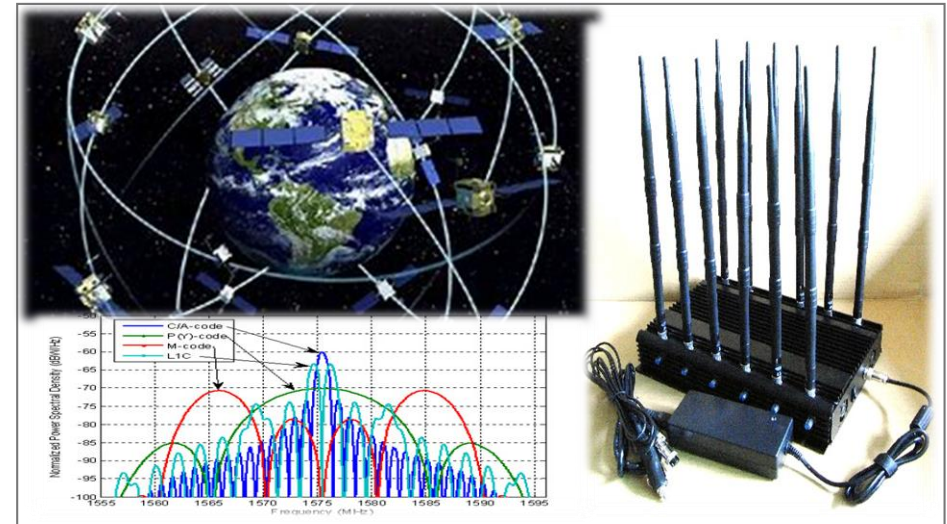

Sponsor: CG-NAV
Stakeholder(s): CG-68, CG-761, CG-791, C4IT SC, C3CEN, NAVCEN, DHS S&T (FRD)

Project #: 2218
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques & Procedures

Notes:

- Legislative requirement.
- Partner with U.S. Army Communications-Electronics Research, Development and Engineering Center and Air Force Research Laboratory.
- Continue working with DHS S&T (FRD) PNT Program.
- Leverage GPS/AIS results from RDC Project 8502: Cybersecurity Vulnerabilities, Threats, and Risk Mitigation Strategies for Coast Guard Surface and Air Assets.

RDC Research Lead:
Mr. Jay Spalding

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Intelligence, Surveillance and Reconnaissance (ISR) Enterprise Data Network Study and Analysis

Mission Need: Enable intelligence-driven operations and collaboration for continued decision advantage in support of all U.S. Coast Guard (CG) missions.


Project Objectives:

- Establish the necessary cross-component Joint Requirements Council (JRC) chartered team to support the development and deployment of a U.S. Department of Homeland Security (DHS) enterprise ISR data network solution.
- Support all need validation analyses and mission need objectives to successfully obtain Acquisition Decision Event (ADE) 0 and 1 approvals.
- Perform technology demonstrations (shore, surface, air) as needed to inform mission need documentation deliverables.
- Specifically focus on cyber security related requirements as solution alternatives are analyzed.
- Support development of requisite CG resource proposals.
- Ensure the smooth transition into the Analyze/Select phase of the Acquisition Lifecycle Framework.

Key Milestone / Deliverable Schedule:

Project Start.....	14 Jun 17 ✓
Standup ISR Enterprise Data Network Integrated Product Team.....	24 Nov 17 ✓
★ Capability Analysis Study Plan Tactical DHS ISR Data Network.....	20 Dec 17 ✓
Start Technology Demonstration(s) to Inform Mission Need.....	6 Jun 19 ✓
ISR Enterprise Data Network Concept of Operations (CONOP) Draft delivered to sponsor	25 Feb 20 ✓
★ ISR Enterprise Data Network Capability Analysis Report (CAR).....	23 Mar 20 ✓
★ ISR Enterprise Data Network Mission Needs Statement (MNS).....	Apr 20
★ ISR Enterprise Data Network (Report & Brief).....	May 20
Project End.....	May 20

★ Indicates RDC product.

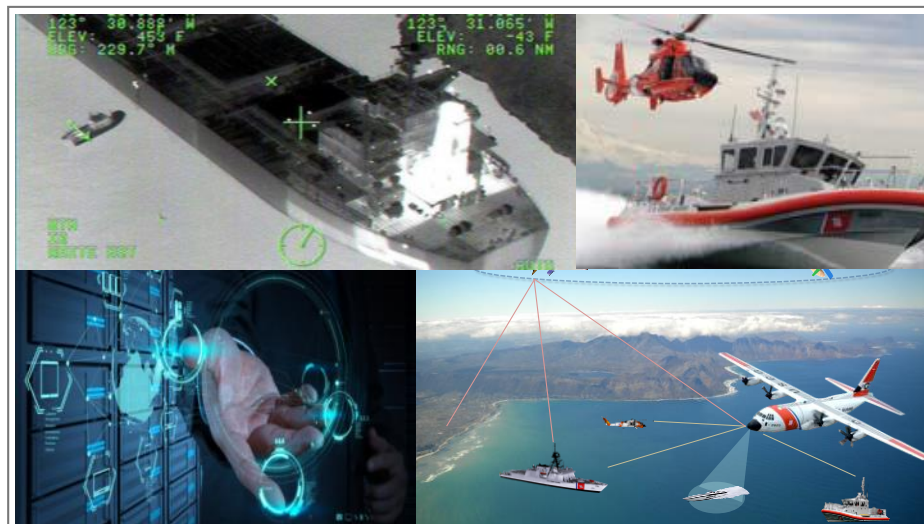

Sponsor: CG-26, DHS S&T (BIM)
Stakeholder(s): CG-93, CG-711/731/741/751/761/791/771, CG-671/68, MIFC, ICC, C4IT SC, CYBERCOM, AREA-6

Project #: 8116	Anticipated Transition: Knowledge Product Acquisition Milestone Support
---------------------------	---

Notes:

- Partner with DHS Science and Technology Directorate (S&T).
- Align with DHS, U.S. Department of Defense, and intelligence community information technology enterprise solutions, including the integrated maritime domain environment.
- Dates for Joint Requirements Integration and Management System documents are contractor deliverable dates and are independent of the JRC timeline for approval.

RDC Research Lead:
LT Anne Newton

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Cybersecurity Vulnerabilities, Threats, and Risk Mitigation Strategies for Coast Guard Surface and Air Assets

Mission Need: U.S. Coast Guard (CG) platforms require resistance and resilience to cyber attacks.

Project Objectives:

- Conduct cyber security risk research analysis for Global Positioning System (GPS), Automatic Identification System (AIS) and specific mission oriented systems dependent on position, navigation and timing.
- Partner with the U.S. Department of Homeland Security Science and Technology Directorate to test specific equipment vulnerabilities and derive the impact and consequence of attacks to identify defense strategies.
- Perform a cyber assessment on a CG asset to identify vulnerabilities, threats and risk mitigation strategies.
- Develop and test a cyber risk mitigation strategy that could be used to recover compromised operational technology systems on CG surface and air assets.

Key Milestone / Deliverable Schedule:

Project Start.....	3 Oct 16 ✓
Inventory and Acquire GPS/AIS Units.....	22 Dec 16 ✓
Conduct GPS/AIS Testing	22 Jul 17 ✓
Inventory Surface Systems for Evaluation.....	26 Oct 17 ✓
★ GPS/AIS Cyber Assessment (Report).....	22 Feb 18 ✓
Conduct Surface Asset Assessment.....	5 Apr 18 ✓
Research Cyber Risk Mitigation Systems at Other Labs.....	31 Oct 18 ✓
Select CG Surface Asset for Cyber Risk Mitigation.....	18 Dec 19 ✓
Develop Cyber Risk Mitigation Strategy in Lab Environment.....	Apr 20
★ Risk Mitigation Strategy (Brief).....	May 20
Conduct Cyber Risk Mitigation Demonstration on CG Cutter.....	May 20
★ Cybersecurity for Coast Guard Surface and Air Assets (Report & Brief).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-791
Stakeholder(s): CG-761, CG-711, CG-751, CG-933, C4ITSC, CYBERCOM

Project #: 8502
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques & Procedures

Notes:

- Leverage research and development efforts of the Office of Naval Research's Resilient Hull, Infrastructure, Mechanical, and Electrical Security program; Federally Funded Research and Development Centers; and University Affiliated Research Centers.
- Partner with Johns Hopkins University Applied Physics Lab on U.S. Navy Sea Change initiatives and cyber risk mitigation.

RDC Research Lead:

Mr. Rob Taylor

CG-926 Domain Lead:

Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Redefine Field Intelligence Reporting and Analysis

Mission Need: Improved information dominance in the maritime domain.

Project Objectives:

- Research cutting edge human language tools, artificial intelligence, machine learning and other analytical tools that can help to automate analysis of field intelligence reports.
- Comprehensively assess intelligence reporting and analyze evaluation processes/constraints within tactical units and intelligence production centers.
- Research government cloud technology that will holistically enable the conditions for shorter feedback loops with relevant, timely, and predictive intelligence for CG decision makers.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Field Collector Summit.....	22 Jan 20 ✓
Intelligence Collection Unit Visits.....	5 Mar 20 ✓
Research Functional Characteristics and Processes.....	Apr 20
Market Research Government Cloud Analytical Tools.....	May 20
★ Redefine Field Intelligence Reporting and Analysis (Report & Brief).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-25
Stakeholder(s): CG-68, CG-5R, CG-CYBER, CG-761
CG-CI, CG-CGIS, ICC, MIFCPAC, MIFCLANT

Project #: 8120	Anticipated Transition: Product Pending Acquisition
---------------------------	---

Notes:

- Partner with the Federal Bureau of Investigation, the U.S. Department of Defense, U.S. Department of Homeland Security Office of Intelligence and Analysis, Office of the Director of National Intelligence, U.S. Immigrations and Customs Enforcement Homeland Security Investigations, as well as other external agencies that we learn about, to study the tools/process they currently use.

RDC Research Lead:
LT Anne Newton

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Maritime Counter Unmanned Aircraft Systems (C-UAS)

Mission Need: Methods to detect, track, identify, and defeat illicit use of unmanned aircraft systems in the maritime environment.

Project Objectives:

- Inform requirements for C-UAS for the U.S. Coast Guard (CG) Ports, Waterways, and Coastal Security and Defense Readiness missions.
- Conduct market research to identify both government off-the-shelf and commercial off-the-shelf technologies that satisfy CG requirements.
- Evaluate system prototypes in an operational maritime environment.
- Integrate successful systems to build an end-to-end layered defensive system prototype, aimed at increasing performance and usability while reducing size, weight and power and manning requirements.
- Provide C-UAS system subject matter expertise in development of tactics, techniques, and procedures for CONUS and OCONUS applications.

Key Milestone / Deliverable Schedule:

Project Start..... 3 Oct 16 ✓

★ **Maritime Counter Unmanned Aircraft Systems (Brief)..... 10 Mar 20 ✓**

Integrated Components Extended User Evaluation..... Sep 20

★ **C-UAS Test & Evaluation Report for the PWCS Mission (Report) Nov 20**

Project End..... Nov 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-MSR
Stakeholder(s): CG-711, CG-731, CG-721, CG-751, DCMS-34, CG-2, CG-6, C3CEN, SFLC, AREA-3, DARPA, DHS S&T

Project #: 7812	Anticipated Transition: Knowledge Product Future Technology
---------------------------	---

Notes:

- This effort will leverage partnerships with the U.S. Department of Homeland Security (DHS) Science and Technology Directorate (S&T), Defense Advanced Research Projects Agency (DARPA), Air Force Research Laboratory, Naval Surface Warfare Centers, the Office of Naval Research, and other government organizations.

RDC Research Lead:
Ms. Amy Cutting

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Performance of Daytime Distress Signals

Mission Need: Determine effectiveness of existing daytime distress signals.

Project Objectives:

- Provide the Office of Design and Engineering Standards empirically-derived information to update distress signal carriage requirements.
- Determine effectiveness of presently-approved daytime distress signals.
- Determine if an enhanced, 2-color, quick-flashing SOS electronic visual distress signal will be effective in daytime.
- Determine if project results can apply to Safety of Life at Sea (SOLAS) guidelines.



Key Milestone / Deliverable Schedule:

Project Start.....	2 Apr 18 ✓
Pilot Testing.....	29 Aug 18 ✓
Field Experiment.....	7 Nov 18 ✓
Key Decision Point: SOLAS Equivalence.....	28 Feb 19 ✓
★ Daytime Distress Signal Effectiveness.....	5 Dec 19 ✓
Project End	5 Dec 19 ✓

Sponsor: CG-ENG

Stakeholder(s): CG-SAR, CG-BSX

Project #: 11011	Anticipated Transition: Knowledge Product Standards/Regulations
----------------------------	---

Notes:

- Follow-on to Project 1101, Alternatives to Pyrotechnic Distress Signals Project.

RDC Research Lead:
LT Liz Murphy

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Develop an Environmentally Friendly Buoy Mooring System

Mission Need: A buoy mooring system for environmentally sensitive areas that would avoid directly damaging nearby delicate plants and animals in the benthic zone.

Project Objectives:

- Conduct market research to determine alternatives to traditional buoy mooring systems.
- Develop and test prototypes to determine best buoy mooring technology for environmentally sensitive areas.



Key Milestone / Deliverable Schedule:

Project Start	10 Nov 14 ✓
Conduct Market Research.....	25 Feb 15 ✓
Key Decision Point: Broad Agency Announcement or Prize Competition.....	14 Oct 15 ✓
Key Decision Point: Prototype Development.....	2 Jun 16 ✓
Demonstration Start.....	3 Apr 18 ✓
★ Environmentally Friendly Buoy Mooring System Deployment (Report).....	14 Aug 18 ✓
Demonstration End.....	14 Jun 19 ✓
★ Environmentally Friendly Buoy Mooring System Deployment (Report).....	14 Nov 19 ✓
★ Environmentally Friendly Buoy Mooring System (Report).....	3 Mar 20 ✓
Project End	3 Mar 20 ✓

★ Indicates RDC product.

Sponsor: CG-NAV
Stakeholder(s): SILC-WOPL, D7, LANT

Project #: 2702	Anticipated Transition: Fielded Prototype
---------------------------	---

Notes:

- Supports Coral Reef Protection Executive Order 13089.
- Supports the Coast Guard Energy Renaissance Action Plan.

RDC Research Lead:
Ms. Irene Gonin

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
 Internet Release is Authorized

April 2020
 Version date

Vessel of Opportunity Skimming System (VOSS) Technology Market Research

Mission Need: State-of-the-market, logistically supportable VOSS technology.

Project Objectives:

- Research state-of-the-market technologies that can potentially replace the current VOSS equipment.
- Ensure VOSS technologies will be operable in D14/D17 Areas of Responsibility (AOR).
- Compile a report for possible future actions related to VOSS equipment replacement.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 18 ✓
Capability Assessment/Mission Needs	18 Mar 19 ✓
Revise Tentative Baseline and Desired Functional Characteristics..	18 Sep 19 ✓
Issue Request for Information (RFI).....	19 Nov 19 ✓
Receive RFI Responses.....	30 Dec 19 ✓
Finalize Market Research.....	26 Feb 20 ✓
★ Vessel of Opportunity Skimming System Technologies Market Research (Report) Jun 20	
Project End.....	Jun 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-MER
Stakeholder(s): CG-751, CG-43, National Strike Force Coordination Center, PACAREA

Project #: 4212
Anticipated Transition: Knowledge Product Acquisition Milestone Support

Notes:

- Oil Spill Liability Trust Fund funding.

RDC Research Lead:
Mr. Alexander Balsley, P.E.

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Oil Sands Products Spill Response

Mission Need: Research and develop enhanced decision-making tools and recovery/mitigation tools for responding to spilled oil sands products.

Project Objectives:

- Analyze and assess behavior, response issues and strategies in fresh and salt waters; and develop tactics and/or technologies that address gaps.
- Provide decision making/job aid tools for U.S. Coast Guard (CG) and commercial responders to aid in response planning and execution for spills of oil sand products in fresh and salt water.



Key Milestone / Deliverable Schedule:

Project Start	31 Aug 14 ✓
★ Response to Oil Sands Products Assessment (Report).....	29 Sep 15 ✓
★ Underwater Sediment Sampling Research (Report).....	19 Jan 17 ✓
★ Testing of Oil Sands Products Recovery in Fresh Water (White Paper)	2 Apr 18 ✓
Bottom Mitigation Techniques Part 2 First Inland Test.....	26 Apr 18 ✓
Bottom Mitigation Techniques Part 2 Offshore Test.....	31 May 18 ✓
Bottom Mitigation Techniques Part 2 Second Inland Test.....	4 Apr 19 ✓
★ Mitigation of Oil Moving Along the Waterway Bottom (Report) ..	14 Nov 19 ✓
Consolidate Project Findings.....	Apr 20
★ Oil Sands Products Spill Response (Report).....	Jul 20
Project End	Jul 20

★ Indicates RDC product.

Sponsor:

CG-MER

Stakeholder(s): EPA, AREA-54, NOAA

Project #:
4705

Anticipated Transition: Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Multiple funding sources including Oil Spill Liability Trust Fund and FY17-18 Great Lakes Restoration Initiative.
- Cooperative Research and Development Agreement with Enbridge Pipeline.
- Leverage research done by academia, U.S. Department of Energy Labs, and international academic institutions.

RDC Research Lead:

Mr. Alexander Balsley, P.E.

CG-926 Domain Lead:

Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

20

Ballast Water Management (BWM) Research and Development

Mission Need: Reduce Nonindigenous Invasive Species (NIS) transport risks by commercial vessels in U.S. waters, including the Great Lakes (GL).

Project Objectives:

- Determine the most practical BWM practices for Laker operators to reduce the risks of transporting NIS from one region of the GL to another when they are introduced from the outside by ocean-going ships.
- Research and develop robust, science-based technical Quality Assurance (QA) protocols to validate sub-Independent Lab (IL) QA/Quality Control shipboard test programs that support BWM System Type Approval (TA).
- Determine the availability and capabilities of existing technologies that field inspectors could use to verify compliance with the Ballast Water Discharge Standard (BWDS).
- Analyze the CG BWM Program impacts on GL invasion rates.

Key Milestone / Deliverable Schedule:

Project Start (FY17-18 Scope of Work).....	1 Oct 17	✓
FY17-18/FY18-19 Great Lakes Restoration Initiative Scope (Remaining)		
★ Ballast Water Management Alternatives for Lakers (Report)...	31 Mar 20	✓
★ IL Auditing Protocol For Facilities Performing TA Testing of BWM Systems (Report).....	Apr 20	
FY19-20 Great Lakes Restoration Initiative Scope		
★ Current State of BWDS Compliance Technologies (Report).....	Sep 20	
★ Functional Char. for BWDS Compliance Tools (Report).....	Sep 20	
★ Technical Guidance for Use, Maintenance, and Training of BWDS Compliance Tools (Report).....	Dec 20	
★ Sampling Plan for Invasion Rates of NIS in the GL (Report).....	Dec 20	
★ Audit Protocols for Shipboard Tests by ILs (Report).....	Jul 21	
★ Evaluation of Commercially Available BWDS Compliance Technologies (Report).....	Jul 21	
Project End (FY17-20 Scope of Work).....	Jul 21	

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-OES, Great Lakes National Program Office

Stakeholder(s): Marine Safety Center, CG-CVC

Project #: 4135	Anticipated Transition: Knowledge Product Standards/Regulations
---------------------------	---

Notes:

- Great Lakes Restoration Initiative funding (DW-070-20000108-0).
- Collaboration with Naval Research Laboratory.
- Collaboration with Smithsonian Environmental Research Center.
- Collaboration with the DOT Maritime Administration and Canadian Dept. of Fisheries & Oceans and Transport Canada.

RDC Research Lead:
Ms. Gail Roderick

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Advancing UAS and AUV Capabilities to Characterize Water Column and Surface Oil in Ice Environments

Mission Need: Technologies to detect and characterize oil spills in ice environments.


Project Objectives:

- Coordinate and conduct lab and field tests of Long Range Autonomous Underwater Vehicle (LRAUV), Remote Environmental Monitoring Units, Autonomous Underwater Vehicles (AUV) and Unmanned Aircraft Systems (UAS) in ice conditions to verify accuracy of sensors and unmanned systems.
- Test the transfer of sensor data in a timely manner to responders and/or Incident Command Post for actionable information.
- Partner with National Oceanic and Atmospheric Administration (NOAA) and others to build on previous tests with UAS and AUV sensors.

Key Milestone / Deliverable Schedule:

Project Start.....	23 Jan 20 ✓
Develop Interagency Reimbursable Work Agreement with NOAA.....	Apr 20
Phase 1: Conduct UAS/AUV Tests at Cold Regions Research and Engineering Laboratory (CRREL).....	Dec 20
Conduct Field Exercise Planning.....	Jan 21
★ UAS/AUV Lab Experiments Results (Report).....	Mar 21
Phase 2: UAS/AUV Systems Field Testing in Great Lakes or Arctic.....	Mar 21
Develop Data Schema for Data Stream Export	May 21
★ UAS/AUV Systems Field Exercise Integration (Report)	Sep 21
Project End.....	Sep 21

★ Indicates RDC product.

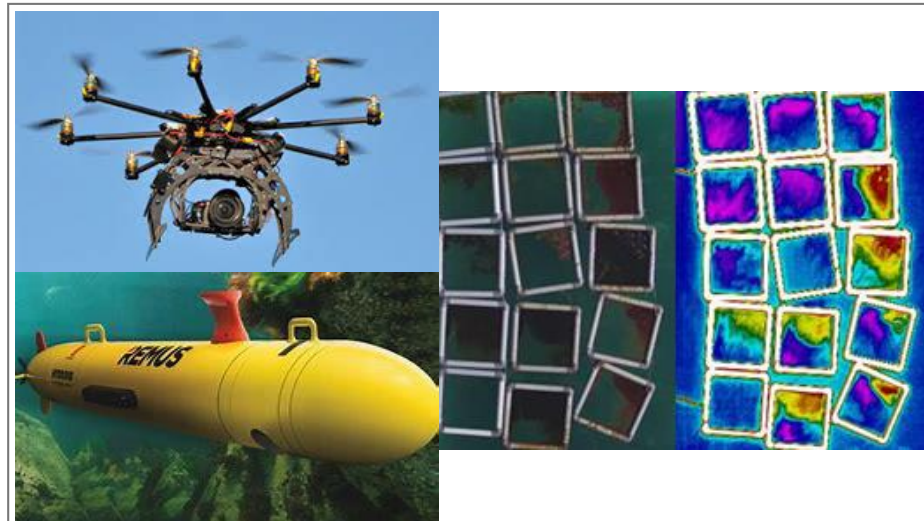

Sponsor: CG-MER
Stakeholder(s): RDC, CG-5RI, D1, D9, D17, ADAC, NOAA OR&R, WHOI, MBARI, DHS S&T OUP

Project #: 4711	Anticipated Transition: Product Fielded Prototype
---------------------------	---

Notes:

- Oil Spill Liability Trust Fund funding.
- Partnerships with CRREL, Woods Hole Oceanographic Institute, Arctic Domain Awareness Center, NOAA, Bureau of Safety and Environmental Enforcement, and U.S. Environmental Protection Agency.
- Possible collaboration with Norwegian Coastal Administration.

RDC Research Lead:
Mr. Alexander Balsley, P.E.

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Survival Modeling, Reporting, and Statistics

Mission Need: Improve Search and Rescue Optimal Planning System (SAROPS) utility by ensuring appropriate incorporation of better survival modeling and statistics.

Project Objectives:

- Research the state of survival modeling, including the availability of “3rd generation” human-thermal models, and their ability to accurately predict ranges of survival time in waters warmer than 15°C (59°F).
- Determine whether the existing Probability of Survival Decision Aid or other models can account for, or incorporate, factors and parameters beyond heat production and heat loss.
- Identify and implement strategies to adapt model(s) to include additional parameters.
- Develop a survival database to validate model(s) against statistics.
- Deliver a survival-model module for plug-in application to the SAROPS.


Key Milestone / Deliverable Schedule:

Project Start.....	1 Nov 17 ✓
<u>Phase I: Survival Model Investigation and Statistics</u>	
Investigate Requirements and Applications.....	30 Apr 18 ✓
Investigate State of Survival Models.....	6 Jul 19 ✓
Conduct Facilitated Workshop	28 Aug 19 ✓
Survival Statistics Brief	16 Dec 19 ✓
Monitor Survival Information Data Collection.....	Jul 20
Key Decision Point to Progress to Model Implementation and Validation.....	Aug 20
<u>Phase II: Survival Model Implementation</u>	
Adapt Model with Prioritized Survival Factors	Mar 21
Validate Survival Model.....	Jul 21
Enhanced CG Survival Model and Implementation Guidance (Report).....	
Sep 21	
Project End.....	Sep 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

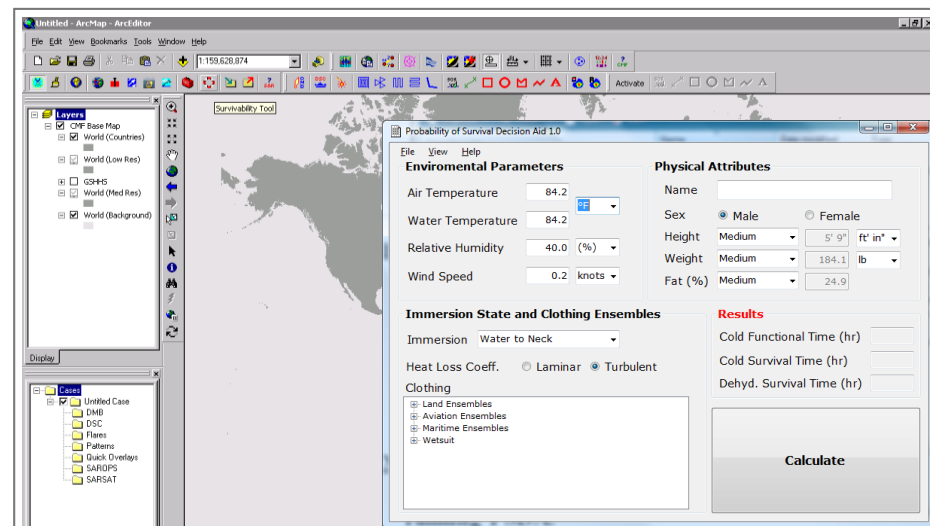

Sponsor: CG-SAR

Stakeholder(s): CG-5R, CG-761, C3CEN, AREA-5

Project #: 1008
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Carries forward U.S. Coast Guard (CG) Research and Development Center survival-related work with U.S. Department of Defense labs.
- Potential efficiencies in saving lives while reducing time on sortie.
- Explore partnerships with National Labs and University Centers.

RDC Research Lead:
Ms. Monica Cisternelli

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

In-Situ Burn (ISB) Research

Mission Need: Improve ISB techniques, technology and monitoring to make ISB a more effective, practical and safe option for oil spill response.

Project Objectives:

- Determine best practices for operational use of ISB.
- Conduct literature review to investigate remote air-monitoring technologies.
- Develop and test procedures to support freshwater ISB of heavy oils with and without contaminated vegetation.
- Conduct air quality monitoring of smoke plumes during ISB field tests and compare with SMART protocol.
- Report results for reference by U.S. Coast Guard (CG) federal on-scene coordinators, regional response teams, agency partners, academia, national labs, and international stakeholders that addresses ability of technology to improve responder safety and increase sampling accuracy.

Key Milestone / Deliverable Schedule:

Project Start	1 Oct 18 ✓
Mesoscale Freshwater Burns	19 Jul 19 ✓
Large-scale Freshwater Burns	25 Oct 19 ✓
Remote Air Monitoring Market Research.....	Jun 20
★ Freshwater In-Situ Burn (Report).....	Jun 20
Develop Remote Air Monitoring Process Framework.....	Jul 20
Develop Test Plan for Remote Air Monitoring.....	Jul 20
Remote Air Monitoring During ISB (tentative).....	Sep 20
Remote Air Monitoring During ISB (tentative).....	Mar 21
★ Remote Air Monitoring Technology Evaluation (Report).....	Nov 21
Project End.....	Nov 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: Great Lakes National Program Office, CG-MER
Stakeholder(s): CG-721, NSF, EPA, BSEE, LANT, PAC, D9, RRT5

Project #: 47041	<u>Anticipated Transition:</u> Knowledge Product Future Technology
----------------------------	--

Notes:

- Multiple funding sources including Oil Spill Liability Trust Fund and Great Lakes Restoration Initiative.
- Partner with academia and national labs to ensure result visibility and access.

RDC Research Lead:
LT Liz Murphy

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Mass Rescue Lifesaving Appliance (MRLSA)

Mission Need: Lightweight, easy to use, temporary, mass rescue survivor platform.

Project Objectives:

- Find, promote, or develop the technology to manufacture an extremely compact, lightweight, rescue intervention device to safely keep 100+ persons out of the water for up to 24 hours.
- Transition the developmental result to the Office of Search and Rescue and capability stakeholders for implementation as a mass rescue tool.



Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Request for Information (RFI)/Technology Assessment.....	1 Mar 20 ✓
★ MRLSA Request for Information Summary (Report).....	Apr 20
Prototype Development	Oct 21
Prototype Evaluation	Nov 21
★ Mass Rescue Lifesaving Appliance (Report).....	Mar 22
Project End.....	Mar 22

★ Indicates RDC product.

Sponsor: CG-SAR
Stakeholder(s): CG-711, CG-731, CG-751

Project #: 1205	<u>Anticipated Transition:</u> Product Fielded Prototype
---------------------------	---

Notes:

- Partnership with Air Force Research Laboratory.
- Investigate National Aeronautics and Space Administration or other government agency partnership.
- Potential use of a Cooperative Research and Development Agreement, or other non-traditional approaches (U.S. Department of Homeland Security Prize Competition) if the RFI does not yield results.

RDC Research Lead:
Ms. Monica Cisternelli

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

25

Nearshore and Inland Evaluation of the Estimated Recovery System Potential (ERSP) Calculator

Mission Need: An ERSP calculator to include response systems for the entire nearshore and inland operating environment.

Project Objectives:

- Research the viability of the current ERSP and the calculator's initial impact in the offshore oil spill response industry.
- With industry and interagency (U.S. Environmental Protection Agency) representatives, assess ERSP as a whole to determine if it effectively rectifies the Economic and Development Review Committee's challenges experienced during Deepwater Horizon.
- Research inland and nearshore oil recovery equipment and efficiencies.
- Research if ERSP can be expanded to include the entire nearshore and inland operating environment.
- Expand ERSP to include inland and nearshore recovery modeling in calculator.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 16 ✓
Feasibility Workshop.....	21 Jun 17 ✓
★ Feasibility of Extending the ERSP Calculator for Nearshore and Inland Waterways (Report)	20 Sep 17 ✓
Complete Contract Negotiations for Calculator Design.	18 Aug 18 ✓
Start Development of Conceptual Model.....	1 Apr 19 ✓
★ Inland ERSP Preliminary Factors, Requirements and Conceptual Model (Report)	14 Nov 19 ✓
★ Inland ERSP Operational Environment Calculator (Design Document)	Apr 20
Start Development of Inland ERSP Calculator Software Tool.....	Apr 20
Begin National Academy of Sciences (NAS) Review.....	Jun 20
★ NAS Response Review of Inland ERSP (White Paper)	Mar 21
Begin Revising Inland ERSP Calculator Based on NAS Feedback.....	Oct 21
★ Inland Evaluation of the ERSP Calculator (Prototype & User Guide)	Jul 22
Project End	Jul 22

★ Indicates RDC product.



Sponsor: CG-MER

Stakeholder(s): BSEE, AREA-54

Project #:	Anticipated Transition:	Product
4710	Fielded Prototype	

Notes:

- Oil Spill Liability Trust Fund funding.
- Partner with Bureau of Safety and Environmental Enforcement (BSEE).

RDC Research Lead:

Mr. Alexander Balsley, P.E.

CG-926 Domain Lead:

Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

26

Next Generation Aids to Navigation Buoys & Alternative Moorings

Mission Need: Reduce U.S. Coast Guard (CG) Aids to Navigation (AtoN) buoy costs, increase buoy reliability and longevity, and moor buoys in an environmentally friendly way.

Project Objectives:

- Perform market study and document existing buoy types and specifications:
 - Consider hard shell plastic, fiberglass and different-shape buoys.
 - Develop a catalog for continued CG use.
- Develop standardized stretch hose mooring technology for all coastal buoy environments.
- Perform field test to determine optimal buoy replacement & mooring options:
 - Obtain the most promising buoys/moorings for exposed, semi-exposed, protected, river, and ice.
 - Deploy each type in proper environment, evaluate performance & document.
 - Provide functional characteristics for next generation buoys.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Complete World Wide Market Study of Buoys.....	31 Mar 20 ✓
Gather Feedback from CG Waterways Operations Product Line, District Five, District Seven, and the Office of Navigation (CG-NAV) Systems on Market Study.....	Jun 20
Obtain Most Promising Buoys for Testing.....	Aug 20
★ Results of Survey/Market Study (Report)	Sep 20
Test Plan for Buoys and Moorings.....	Oct 20
Perform Engineering Design and Fabrication of Alternative Moorings.....	Jan 21
Field Test for Buoys and Moorings	Oct 22
★ New Buoy Field Trial & Alternative Moorings Summary (Report).....	Jul 23
Project End.....	Jul 23

★ Indicates RDC product.



Sponsor: SILC-WOPL

Stakeholder(s): CG-NAV, Districts

Project #: 2703	Anticipated Transition: Knowledge Product Acquisition Milestone Support
------------------------	--

Notes:

- Establish Cooperative Research and Development Agreements with vendors willing to work with the CG Research and Development Center for mutual benefit.
- Coordinate with CG-NAV and CG Director of International Affairs and Foreign Policy to involve International Association of Marine Aids to Navigation and Lighthouse Authorities as partners.

RDC Research Lead:
Ms. Irene Gonin

CG-926 Domain Lead:
Ms. Karin Messenger

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

CG Nearshore Use of FirstNet

Mission Need: Interoperable voice and high speed data communications among Sector Forces and First Responders within Sea Area A1 (within 20 nautical miles of shore).

Project Objectives:

- Leverage a Cooperative Research and Development Agreement (CRADA) to investigate U.S. Coast Guard (CG) operational use of the National Public Safety Broadband Network (commonly called FirstNet).
 - Assess the feasibility and effectiveness of leveraging CG infrastructure (e.g., Rescue 21 towers) to enhance FirstNet designs.
 - Adapt 4G/LTE technology for the maritime environment to best support the CG, public safety, U.S. Department of Defense, and Other Government Agencies within 20 nautical miles of shore.
- Phase 1:* Deploy handsets, FirstNet Enhanced Push To Talk (EPTT), blue force tracking, and Geosuite.
- Phase 2:* Optimize radio access network, FirstNet integrated dispatch console, and EPPT enhanced equipment.
- Phase 3:* Deploy Band 14 vessel routers.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Mar 18 ✓
Limited User Evaluation Start.....	1 Feb 19 ✓
CG FirstNet Maritime Test Range: Phase 1	1 Feb 19 ✓
CG FirstNet Maritime Test Range: Phase 2	19 Aug 19 ✓
★ Coast Guard Nearshore Use of FirstNet (Brief).....	22 Nov 19 ✓
CG FirstNet Maritime Test Range: Phase 3	31 Jan 20 ✓
Sector Key West Full Scale Exercise	11 Mar 20 ✓
Limited User Evaluation.....	31 Mar 20 ✓
★ Coast Guard Nearshore Use of FirstNet: Test Results and Recommendations (Report & Brief).....	May 20
Project End.....	May 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-67
Stakeholder(s): CG-255, CG-721/31/41/51/61/91, C4IT SC
 LANT/PAC-6, C3CEN, TISCOM, D7, JIATF

Project #: 58041	Anticipated Transition: Product Fielded Prototype
----------------------------	---

Notes:

- Project includes use of a CRADA.
- Partners: FirstNet Program Office, U.S. Customs and Border Protection Office of Air and Marine, and Florida Fish and Wildlife Conservation Commission.

RDC Research Lead:
Mr. Jon Turban, P.E.

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Evaluation of Potential CG Use of CubeSats

Mission Need: Investigation and assessment of the operational utility of CubeSat technology for U.S. Coast Guard (CG) missions.


Project Objectives:

- Develop and deploy two ground stations for the Mobile CubeSat Command and Control (MC3) ground network, test and document the performance of the MC3 ground stations.
- Participate/partner in CubeSat technology development, test and document CubeSat performance during on-orbit test and evaluation of Polar Scout.
- Perform a CubeSat payload mission assessment that includes CubeSat concept of operations scenarios that would support CG mission needs and influence CubeSat requirements.
- Prepare a CubeSat technology roadmap to support the most pressing CG mission needs, including development, deployment and operations and maintenance planning factors.

Key Milestone / Deliverable Schedule:

Project Start.....	29 Jun 16 ✓
Partner Collaboration/Integrated Product Team Establishment...	25 Oct 16 ✓
Deploy MC3 Ground Station (Fairbanks, AK).....	26 Sep 17 ✓
★ Performance Test Results of Fairbanks Polar Scout Ground Station (Report)	20 Aug 18 ✓
★ Coast Guard Use of CubeSat Technology (Brief)	24 Nov 18 ✓
Polar Scout Launch.....	3 Dec 18 ✓
Deploy MC3 Ground Station (New London, CT).....	26 Jan 19 ✓
Polar Scout Demonstrations Begin.....	1 May 19 ✓
★ Performance Test Results of New London Polar Scout Ground Station (Report).....	1 Jul 19 ✓
Polar Scout Mission Concludes.....	31 Jan 20 ✓
★ Coast Guard Use of CubeSat Technology Assessment and Roadmap (Report)	Aug 20
Project End.....	Aug 20

★ Indicates RDC product.

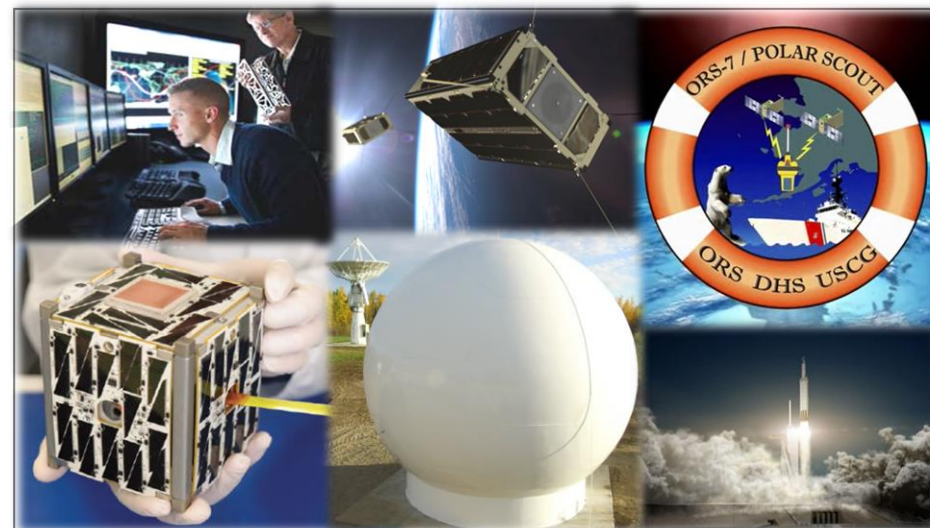

Sponsor: CG-SAR
Stakeholder(s): DHS S&T (BIM), CG-25, CG-26, CG-761, CG-771, CG-MLE, CG-MER3, IIP, D17, CGA

Project #: 7759	Anticipated Transition: Product Fielded Prototype
---------------------------	---

Notes:

- Partner with U.S. Department of Homeland Security Science & Technology Directorate, U.S. Air Force Space Rapid Capabilities Office, National Oceanic and Atmospheric Administration, Naval Postgraduate School, and CG Academy to launch and evaluate CubeSat technology.
- Collaborate with Air Force Institute of Technology, U.S. Navy Program Executive Office Space Systems, and other agencies.
- Leverage Lawrence Livermore National Laboratory.

RDC Research Lead:
LCDR Grant Wyman

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Iceberg Detection and Information Dissemination Methods

Mission Need: Improve quality of iceberg detection using satellite images and improve customer information dissemination.

Project Objectives:

- Research product dissemination methodologies for current International Ice Patrol (IIP) Iceberg Limit product.
- Improve current dissemination and shape requirements/limitations for future products.
- Develop additional products which provide more information to the maritime public regarding navigation risks posed by icebergs.
- Act as the U.S. Coast Guard (CG) Research and Development Center (RDC) liaison to the Department of Homeland Security (DHS) Science and Technology Directorate (S&T) Iceberg Tagging effort.
- Develop understanding of the application of machine learning to iceberg detection in Sentinel 1 satellite images.


Key Milestone / Deliverable Schedule:

Project Start.....	1 Apr 19 ✓
Effort I Start.....	1 Apr 19 ✓
Effort II Start.....	1 May 19 ✓
Document Current Iceberg Product Development.....	18 Aug 19 ✓
Evaluate output of DHS S&T Iceberg Tagging Effort	30 Sep 19 ✓
Investigate New Distribution Process.....	3 Jan 20 ✓
Tracking Data Usage.....	3 Feb 20 ✓
Investigate Machine Learning.....	May 20
Identify New Products.....	Jun 20
★ Iceberg Product Dissemination/Development (Report).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

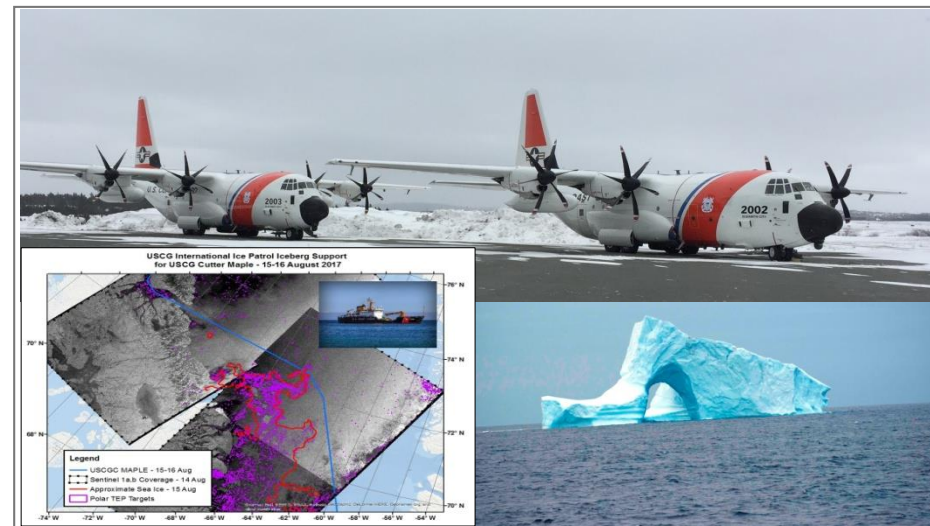

Sponsor: CG-WWM
Stakeholder(s): IIP, CG-5PW, CG-711, Air Station Elizabeth City, LANTAREA

Project #: 6509
Anticipated Transition: Knowledge Product
Acquisition Milestone Support

Notes:

- Supports Safety of Life at Sea.
- Leverage DHS S&T Iceberg Tagging effort.
- Supports CGA Capstone: Machine Learning for Data Dissemination.

RDC Research Lead:
Mr. Jack Cline

CG-926 Domain Lead:
Vacant


*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Automatic Identification System (AIS) Cyber Security

Mission Need: Improve mariner safety by hardening the AIS against cyber attacks.

Project Objectives:

- Investigate existing national and international cryptography research for data message authentication.
- Investigate previous signal bit-level research on extending AIS range to possibly address cybersecurity through signal verification of radio frequency information (AIS 2.0).
- Research Nationwide AIS data machine learning implementations that could augment AIS monitoring and alerting.
- Trial and demonstrate promising efforts.
- Report results and recommendations to support future implementation.

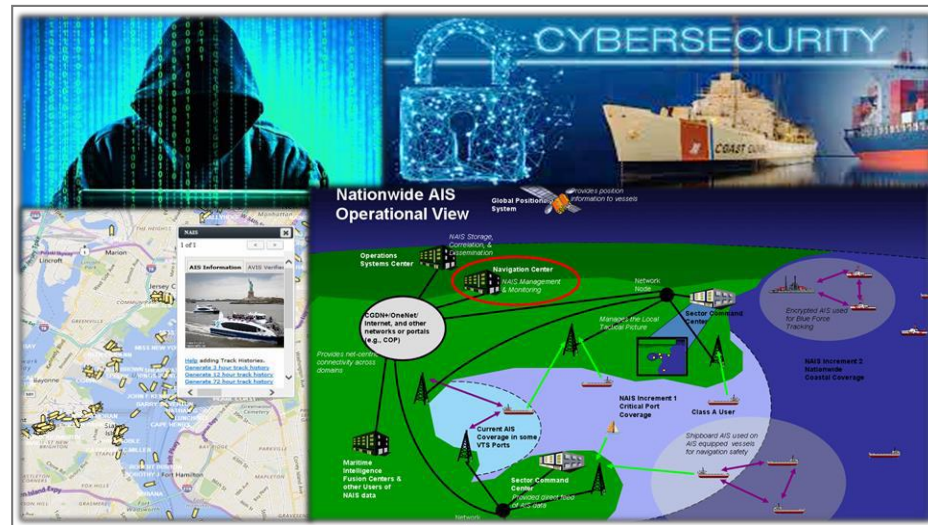

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19	✓
--------------------	----------	---

Research Encryption Methods Proposed Internationally..... May 20

AIS 2.0 Capability Demonstration Aug 20

★ AIS Data Authentication (Brief)..... Aug 20

AIS Machine Learning Analysis Sep 20

Lab Demonstration of AIS Cyber Attack Defense & Mitigation.... Oct 20

★ AIS Signal Verification (Brief)..... Oct 20

★ AIS Machine Learning (Brief) Dec 20

★ AIS Cyber Security (Report)..... Jun 21

Project End..... Jun 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

31

Sponsor:	CG-761
Stakeholder(s):	CG-68, CGCYBER, CG-761, CG-NAV, ICC, MIFCLANT/PAC, CGA

Project #:	<u>Anticipated Transition:</u>	Knowledge Product
8701	Standards/Regulations	

Notes:

- Possible partnership with Naval Postgraduate School.
- Leverage RDC Project 2218, Countering GPS Interference, and Project 6211, Next Generation Arctic Navigational Safety Information System.
- Leverage the U.S. Department of Homeland Security Homeland Security Systems Engineering and Development Institute/MITRE for machine learning analysis.

RDC Research Lead:
Mr. Jay Spalding

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Evaluate Network Accelerator Technology to Improve Cutter Information Technology (IT) Performance

Mission Need: Hardware and software solutions to improve cutter IT performance.

Project Objectives:

- Review background issues and previous/current U.S. Coast Guard (CG) efforts to document and improve cutter IT application performance.
- Evaluate commercially available equipment that could improve network performance in a degraded, or high-latency environment.
- Perform limited user evaluation of selected equipment on an afloat unit.
- Investigate best practices, including transition to the cloud, to improve IT performance in a degraded, disconnected and high latency environment.
- Perform market research for CG database presentation tools to potentially support next generation Enterprise Service Bus (ESB).
- Make recommendations to sponsor and stakeholders about ways to most improve cutter IT application performance.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Review of CG Previous/Current Efforts	31 Dec 19 ✓
Evaluate Network Accelerator Technology	28 Feb 20 ✓
Limited User Evaluation of Selected Equipment	Jul 20
★ Network Accelerator Tech Evaluation (Brief)	Oct 20
Investigate Best Practices for Software	Mar 21
Perform Market Research for Next Generation ESB	May 21
★ Improve Cutter IT Application Performance (Report)	Jul 21
Project End.....	Jul 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-68

Stakeholder(s): CG-761, C4IT SC, CG-67, CGCYBER

Project #: 8702	<u>Anticipated Transition:</u> Knowledge Product Acquisition Milestone Support
---------------------------	--

Notes:

- Potential Cooperative Research and Development Agreement for commercial technology tested aboard U.S. Navy ships.
- Potential partnerships with Johns Hopkins Applied Physics Laboratory, Argonne National Lab, and Los Alamos National Lab (APEX Facility).

RDC Research Lead:
Mr. David Cote

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Radio Frequency (RF) Communications in a Cloud Environment

Mission Need: RF communications capabilities as virtualized services in a cloud environment.

Project Objectives:

- Satisfy existing RF Comms requirements by leveraging CG network infrastructure along with Coast Guard One View (CG1V) and approved Cloud Access Points.
- Investigate the cloud service, architecture, and implementation that provides the best solution for replacing existing RF Comms components in the Rescue 21 (R21) system.
- Replace existing backend server components currently deployed at R21 Remote Fixed Facilities and Sector Command Centers with cloud-based capabilities and perform system demonstration (Phase 1).
- Replace existing R21 user console with cloud-based web accessible interface and perform system demonstration (Phase 2).
- Assess operational improvements and make NextGen R21 recommendations.

Key Milestone / Deliverable Schedule:

Project Start.....	12 Feb 20 ✓
Establish Cooperative Research and Development Agreement (CRADA)	21 Jan 20 ✓
Design System Architecture.....	27 Mar 20 ✓
Establish Cloud Environment	Jun 20
Deploy and Connect Phase 1 R21 Cloud Prototype.....	Jul 20
Initiate Phase 1 Testing	Aug 20
★ RF Comms Cloud Suitability Phase 1 (Brief).....	Nov 20
Develop and Deploy Phase 2 User Interface to CG1V.....	Mar 21
Initiate Phase 2 Testing	Apr 21
★ RF Comms Cloud Suitability (Report).....	Sep 21
Project End.....	Sep 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor:	CG-761	
Stakeholder(s):	CG-68, CG-67, CG-741, CG-SAR, C3CEN, CGCYBER	
Project #:	Anticipated Transition:	Product
8503	Fielded Prototype	
Notes:		
<ul style="list-style-type: none"> • Technical design and execution with C3CEN Remote Mission Systems Product Line. • Leverage CRADA with industry. • Coordinate with CG-68 for CG cloud pilot. 		
RDC Research Lead:		CG-926 Domain Lead:
LCDR Grant Wyman		Ms. Holly Wendelin
<p><i>For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil</i></p>		

Extended Reality (XR) Capabilities for Coast Guard Mission Support

Mission Need: Improve the efficiency and effectiveness of maintenance and training across all U.S. Coast Guard (CG) communities.

Project Objectives:

- Identify maintenance, training, tools, processes, and procedures used by military and industry that will enhance the CG's ability to train personnel and perform maintenance on CG assets with the following goals:
 - Reduce the labor burden of technicians by providing current maintenance information via XR technologies.
 - Increase the availability of assets by improving the efficiency of maintenance and reducing costly errors.
 - Improve the effectiveness of training and reduce the time to train personnel.
- Create a roadmap that will enable sponsor to generate requirements and successfully implement extended reality capabilities throughout the CG to improve the performance of mission support services.

Key Milestone / Deliverable Schedule:

Project Start.....	30 Nov 17 ✓
★ Market Research/Technology Assessment (Brief).....	19 Dec 18 ✓
87' WPB Augmented Reality Maintenance Prototype Delivered....	18 Sep 19 ✓
★ Limited User Evaluation - Surface Community (Brief).....	Oct 20
Aviation Augmented Reality Maintenance Prototype Delivered.....	Dec 20
Marine Inspection XR Training Prototype Delivered.....	May 21
★ Limited User Evaluation - Aviation Community (Brief).....	Aug 21
★ Limited User Evaluation - Training Community (Brief)	Jan 22
Mission Support XR Roadmap.....	Mar 22
★ XR Capabilities for CG Mission Support (Report & Brief).....	Jul 22
Project End.....	Jul 22

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: FORCECOM
Stakeholder(s): CG-1B3/41/45/5PC/67/711/731/751/761/933, ALC ATC, ATTC, CGA, SFLC, TRACEN Yorktown

Project #: 8107
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques & Procedures

Notes:

- Includes partnerships with Massachusetts Institute of Technology Lincoln Laboratory, Naval Sea Systems Command Portsmouth Naval Shipyard, Microsoft Technology Center Boston, Avatar Partners, and other U.S. Department of Defense components that have successfully adopted XR technologies in their mission support programs.
- Uses agile scrum development and rapid contracting through Defense Logistics Agency's Tailored Logistic Support Program.

RDC Research Lead:

Mr. Jon Turban

CG-926 Domain Lead:

Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Evaluation and Testing of VHF Data Exchange System (VDES) Impacts on the Automatic Identification System (AIS)

Mission Need: Determine VDES benefits and path to implementation to support U.S. Coast Guard (CG) operations.

Project Objectives:

- Develop a technology roadmap for use of VDES:
 - Perform literature review, investigate the maturity of standards, market research of VDES equipment, analyze findings from worldwide VDES field trials, and identify steps for CG implementation.
- Phase 1 – VDES limited user evaluation to develop a transition plan to:
 - Shift CG tactical data transmissions from AIS channels to proposed frequencies for application specific message channels.
- Phase 2 – VDES limited user evaluation to:
 - Evaluate usage of different VDES channels to support various data types.
 - Investigate operational needs to support shore-side management of VDES.
 - Perform system level testing for frequency interference, limits to system overloads, message reception rates, out-of-bound interference, etc.


Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Technology Roadmap Investigation.....	Sep 20
★ VDES Technology Roadmap (Report).....	Feb 21
Test Plan, Equipment Integration, and Bench Test.....	Mar 21
Phase 1 Field Trials – VDES Limited User Evaluation.....	Sep 21
★ Sensitive but Unclassified Tactical Information Exchange and Display System (STEDS) using VDES (Report).....	Nov 21
Phase 2 Field Trials – VDES Limited User Evaluation.....	Sep 22
★ VHF Data Exchange System Field Trial (Report & Brief).....	Dec 22
Project End.....	Dec 22

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

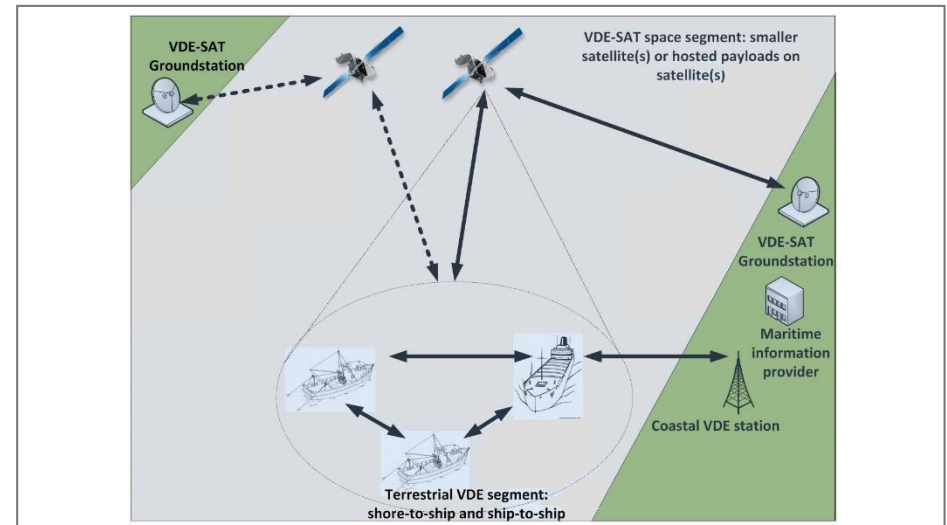

Sponsor: CG-761
Stakeholder(s): CG-67, CG-68, CG-9335, CG-NAV, NAVCEN, C3CEN

Project #: 8703
Anticipated Transition: Knowledge Product
Future Technology

Notes:

- Work closely with the Canadian Coast Guard, Electronics and Information Services, Quebec.
- Leverage prior CG Research and Development Center work completed concerning options and impacts for VDE and AIS.

RDC Research Lead:
Ms. Irene Gonin

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Risk Based Cruise Ship Safety Score

Mission Need: Improve cruise ship risk assessments through a risk assessment score based on a vessel's exam results.

Project Objectives:

- Evaluate current practices to determine a cruise ship's risk for a safety or security incident.
- Working with subject matter experts, evaluate deficiencies (risk and/or consequence) and appropriately categorize deficiencies and assign appropriate weights.
- Develop a prototype, an automated method, to determine a cruise ship's risk assessment via its deficiency exam results and corresponding deficiency category weights.
- Receive feedback from industry on the effectiveness of the prototype's outputs.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 18 ✓
Analysis of Current Practices in Place.....	27 Dec 18 ✓
Categorize and Quantify Deficiency Severity.....	17 Jul 19 ✓
Develop Weighted Deficiency Scoring System.....	30 Sep 19 ✓
Prototype Development and Beta Testing.....	4 Mar 20 ✓
Preliminary Testing and Analysis with Users.....	5 Mar 20 ✓
★ Prototype and Graphical User Interface for the Cruise Ship National Center of Expertise (Prototype & GUI).....	6 Mar 20 ✓
Project End.....	6 Mar 20 ✓

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

36



Sponsor: CG-5P-TI
Stakeholder(s): Cruise Ship National Center of Expertise

Project #: 3502	Anticipated Transition: Product Fielded Prototype
---------------------------	---

Notes:

- Leverages prior U.S. Coast Guard Research and Development Center work related to vessel inspections.

RDC Research Lead:
Mr. Sam Cheung

CG-926 Domain Lead:
CDR James Small

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Ice Condition (ICECON) Risk Assessment Tool(s)

Mission Need: Method to forecast and share ice conditions.

Project Objectives:

- Develop ICECON classification methodology.
- Develop ship classifications for Great Lakes.
- Validate ice and ship classifications with observed conditions.
- Develop ICECON nowcast and forecast methodology.
- Adjust forecast methodology with icebreaker activity.
- Provide ICECON forecast system for decision support.
- Conduct a feasibility analysis for the development of an Arctic ICECON.


Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 16 ✓
ICECON Workshop.....	29 Nov 16 ✓
★ ICECON Update (Brief).....	22 Sep 17 ✓
★ ICECON Update (Brief).....	15 Oct 18 ✓
★ ICECON Update (Brief).....	2 Oct 19 ✓
ICECON Model Validation.....	Jun 20
★ ICECON Forecast Model (Report & Brief).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

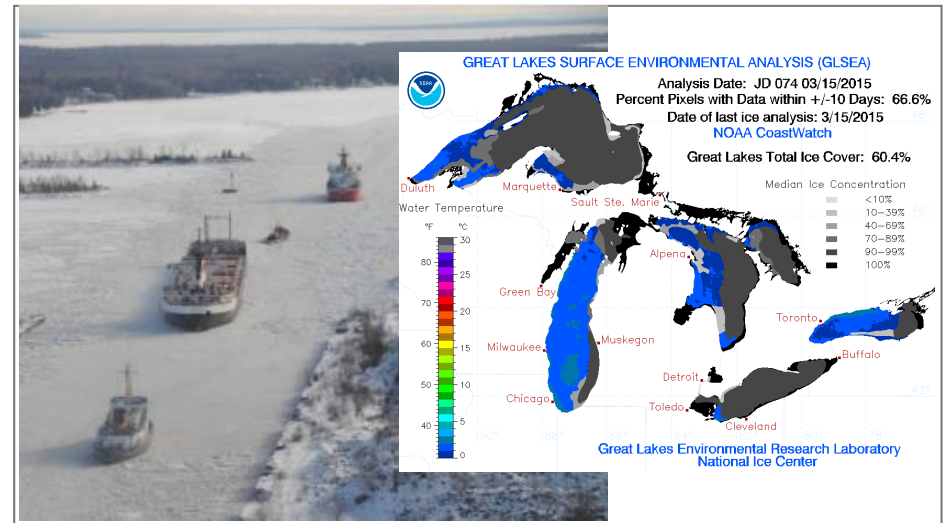

Sponsor: CG-WWM, CG-5PW
Stakeholder(s): National Ice Center, D1, D9, D17, LANT, PAC-5, DHS S&T Office of University Programs

Project #: 6512
Anticipated Transition: Product
Fielded Prototype

Notes:

- Collaboration with Department of Homeland Security Science and Technology Directorate Arctic Domain Awareness Center (ADAC).
- Leverage ADAC Arctic Ice Conditions Index effort.

RDC Research Lead:
Mr. Sam Cheung

CG-926 Domain Lead:
Vacant


*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Research into Navigational Safety Risk Modeling and Analysis Tool

Mission Need: Capability to fully characterize the impact of rerouting traffic, funneling traffic, and placement of offshore structures in terms of risk.

Project Objectives:

- Analytical modeling process and analysis tools to predict changes in traffic patterns and determine the resultant changes in navigational safety risk.
- The ability to assess the proposed wind energy areas to further refine appropriate distances between shipping and structures.
- The ability to assess the need to create routing measures to mitigate risk posed by fixed structures.
- Review Pacific Northwest National Laboratory tool.

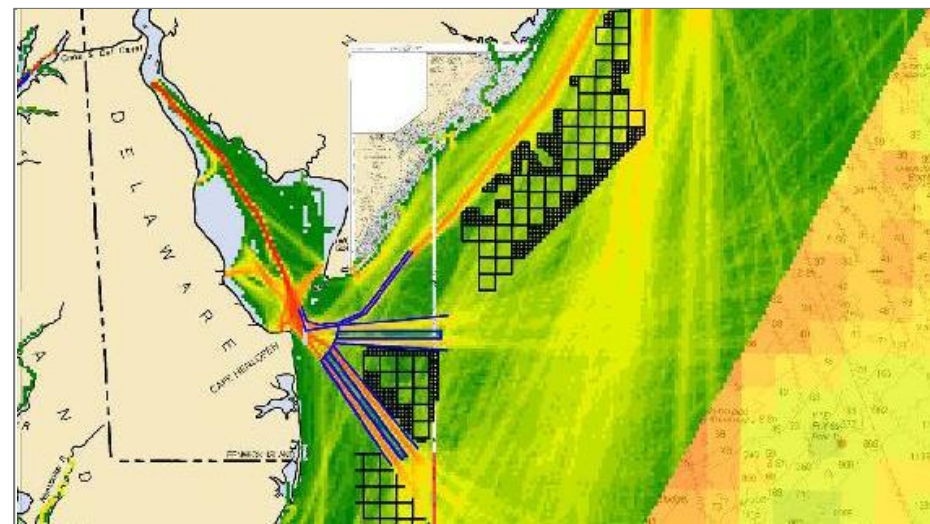

Key Milestone / Deliverable Schedule:

Project Start.....	3 Oct 16 ✓
Assessment of Risk Modeling Tools.....	31 Aug 18 ✓
Automatic Identification System Risk Modeling Data Package.....	5 Dec 18 ✓
Creation of an Offshore Energy Risk Assessment Tool.....	31 May 19 ✓
Test Risk Modeling Package.....	26 Jul 19 ✓
★ Navigational Safety Risk Modeling and Analysis Tool Summary Report (Model & Report).....	6 Nov 19 ✓
Refine Assessment Tool and Methodology	May 20
Full-Scale Process Walk-Through.....	Aug 20
★ Navigational Safety Risk Modeling and Analysis After Action Report (Report).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.

Sponsor: CG-5PW

Stakeholder(s): LANT-54, CG-NAV

Project #: 7529 **Anticipated Transition:** Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Continuation of the Atlantic Coast Port Access Route Study with requirements as documented in the Interim Report from Jul 2012 and the Final Report from Feb 2016.

RDC Research Lead:
Ms. Christine Hansen

CG-926 Domain Lead:
Vacant

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

38

Machine Learning Platforms to Improve Coast Guard Tools

Mission Need: Assess the value of machine learning for improving U.S. Coast Guard (CG) tools.

Project Objectives:

- Identify application areas for implementation of artificial intelligence(AI)/ machine learning (ML) approaches.
- Review the application of AI/ML in the CG, U.S. Department of Defense (DoD) , and U.S. Department of Homeland Security. Determine if any current applications can be usefully applied to additional CG missions.
- Develop a prototype solution for selected application area.



Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
Identify High-level Application Areas for AI/ML Solutions.....	Jun 20
Review USCG, DoD, and DHS Applications of AI/ML Solutions.....	Sep 20
Identify Application Area for Solution Development.....	Oct 20
★ Develop Solution for Selected Application Area (Prototype)....	Feb 21
★ AI/ML to Improve Coast Guard Tools (Report)	May 21
Project End.....	May 21

★
★

★ Indicates RDC product.

Sponsor: CG-771
Stakeholder(s): CG-761

Project #: 7401	Anticipated Transition: Knowledge Product Influence Tactics, Techniques, & Procedures
------------------------	---

Notes:
<ul style="list-style-type: none"> • Potential partnerships with the Air Force Institute of Technology and Naval Postgraduate School.

RDC Research Lead: Ms. Grace Python	CG-926 Domain Lead: Vacant
---	--------------------------------------

For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil

Exploring Machine Learning (ML) for Application In USCG Mission Planning & Disaster Response

Mission Need: Improve the U.S. Coast Guard's (CG) emergency preparedness and increase response effectiveness.

Project Objectives:

- Phase I:
 - Literature research and review: application of Artificial Intelligence (AI) and ML to CG Humanitarian Assistance and Disaster Response (HA/DR). Assess how the use of AI/ML could enhance the efficiency of CG planning and response process during a crisis.
- Phase II:
 - Naval Postgraduate School conducts ML digital image change detection research.
 - University of Illinois (U of I) conducts ML HA/DR network analysis and natural language processing of the 2010 Haiti earthquake response.
- Phase III:
 - Test natural language processing as a tool to harvest analysis data from MISLE SAR narratives.
 - Expand the ML HA/DR network analysis and natural language processing to include U.S. case and compare results to international case.


Key Milestone / Deliverable Schedule:

Project Start.....	20 Oct 17	✓
Phase I - Conduct Literature Review and Assessment.....	30 Apr 18	✓
Initiate Phase II	30 Apr 19	✓
Change Detection of Marine Environments Using Machine Learning (Naval Postgraduate School)		
Thesis A.....	31 Jan 20	✓
Thesis B.....	Apr 20	
U of I Natural Language Processing.....	Jul 20	
★ Machine Learning Exploration: Phase II Results (Brief).....	Aug 20	
Initiate Phase III	Aug 20	
★ Machine Learning for Application in USCG Mission Planning & Disaster Response (Report & Brief)	Aug 21	
Project End.....	Aug 21	

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

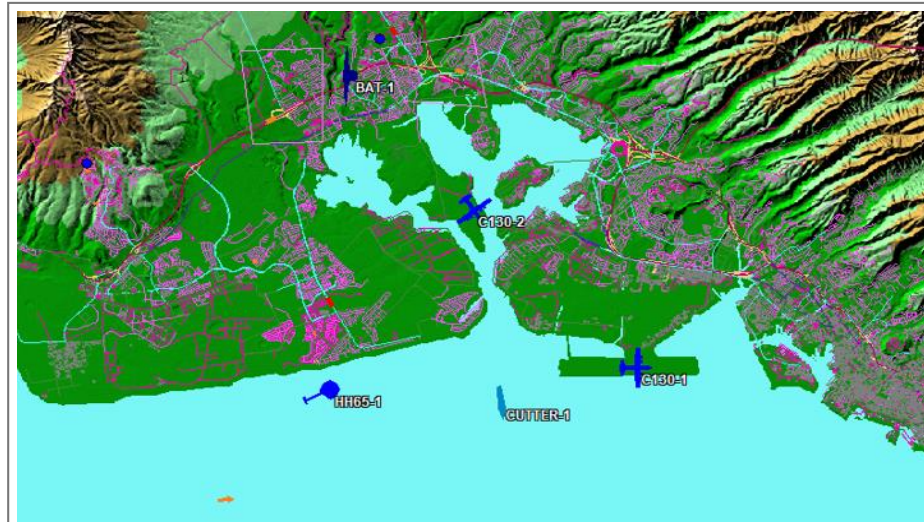

Sponsor: CG-OEM

Stakeholder(s): CG-CVC, CG-MER, CG-2, LANT-35, PAC-53

Project #: 3309	Anticipated Transition: Knowledge Product Future Technology
---------------------------	---

Notes:

- Collaboration with the DHS Center – University of Illinois (Champaign-Urbana).
- Collaboration with the U.S. Department of Defense Joint Artificial Intelligence Center.

RDC Research Lead:
Ms. Christine Hansen

CG-926 Domain Lead:
Vacant

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Condition-Based Maintenance (CBM) for Coast Guard Asset Product Lines

Mission Need: Targeted condition-based and predictive maintenance for higher asset availability, better use of resources, and reduced life cycle costs.

Project Objectives:

- Research significant opportunities for using leading indicators and readily available system information to implement condition-based and predictive maintenance activities within the surface and aviation communities.
- Research system characteristics: interfaces, data structure, data analysis, and data display.
- Conduct market research of available commercial and Governmental Off-The-Shelf (GOTS) systems that accommodate identified system characteristics.
- Provide recommendations for systems and steps required to accommodate functional characteristics.
- Work with research partnerships to develop demonstration case studies using predictive maintenance with Coast Guard data.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Apr 19 ✓
Surface Asset Maintenance Characteristics Review.....	1 Apr 19 ✓
Surface CBM Market Research.....	29 Oct 19 ✓
Academic Partnership Engagements.....	1 Dec 19 ✓
★ CBM for CG Asset Product Lines (Brief)	14 Feb 20 ✓
Aviation Asset Maintenance Characteristics Review.....	15 Feb 20 ✓
★ CBM for CG Surface Assets (Report)	Aug 20
Aviation CBM Market Research	Oct 20
★ CBM for CG Aviation Assets (Report)	Feb 21
★ CBM for CG Asset Product Lines Summary Report (Report)...	Sep 21
Project End.....	Sep 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: CG-45, CG-41

Stakeholder(s): SFLC, ALC

Project #: 9204	Anticipated Transition: Knowledge Product Acquisition Milestone Support
---------------------------	---

Notes:

- Partner with the CG Surface Forces Logistics Center (SFLC) and Aviation Logistics Center (ALC) to make recommendations.
- Potential partnership with GOTS providers, Naval Postgraduate School, Air Force Institute of Technology, Naval Academy, Massachusetts Institute of Technology, DHS S&T Office of University Programs, and Connecticut National Guard.

RDC Research Lead:
Ms. Christine Hansen

CG-926 Domain Lead:
Vacant

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Incorporating Sensor Performance in SAROPS

Mission Need: Time and cost effective methodology to incorporate sensor capabilities in the Search and Rescue Optimal Planning System (SAROPS).

Project Objectives:

- Research and document the SAROPS data requirements related to sensor inputs.
- Determine sensitivity of SAROPS search metrics to inputs.
- Identify a resource-effective approach to develop the sensor-specific data required for use in SAROPS.
- Create a prototype of this new approach for developing the sensor-specific data.

Key Milestone / Deliverable Schedule:

Project Start.....	2 Oct 17 ✓
Completion of Work Under Original Project Scope.....	13 Mar 19 ✓
Project Re-scoped and Retitled	11 Jul 19 ✓
★ Required SAROPS Input to Develop Sweep Width (Brief).....	15 Dec 19 ✓
Key Decision Point.....	16 Dec 19 ✓
Conduct Sensitivity Analysis & Investigate Underlying Assumptions....	Aug 20
★ SAROPS Sensitivity Analysis (Brief).....	Sep 20
Research Novel Methods to Develop Sensor-Specific Data	Apr 21
★ Incorporating Sensor Performance in SAROPS (Interim Report)....	Jun 21
★ Prototype Tool for Incorporating Sensor Performance in SAROPS (Prototype)	Dec 21
★ Incorporating Sensor Performance in SAROPS (Report).....	Feb 22
Project End.....	Feb 22

★ Indicates RDC product.



Sponsor: CG-SAR
Stakeholder(s): LANT, PAC, FORCECOM, D1, D7, D9, D11, D13, Boat Forces

Project #: 7937
Anticipated Transition: Knowledge Product
 Influence Tactics, Techniques, & Procedures

Notes:

- Leverages U.S. Coast Guard Research and Development Center's previous work with developing SAROPS sensor inputs.

RDC Research Lead:
 Ms. Grace Python

CG-926 Domain Lead:
 Vacant

*For more information, call (860) 271-2600 or
 e-mail RDC-Info@uscg.mil*



Acquisition Directorate
 Research & Development Center

UNCLAS/USCG Research & Development Center
 Internet Release is Authorized

April 2020
 Version date

Define and Communicate Exclusion Zones

Mission Need: Capability to physically mark and clearly communicate the boundaries of an area of exclusion, including both fixed and moving security zones.

Project Objectives:

- Review user needs, consider short-term and longer-term solutions.
- Investigate solutions on the market to determine the best possible solutions to evaluate.
- Select and test prototype solution(s) that will unambiguously mark fixed and moving security zones.



Key Milestone / Deliverable Schedule:

Project Start.....	4 Feb 14 ✓
Unit Visit/Market Research Request for Information.....	6 Aug 14 ✓
★ Define and Communicate Exclusion Zones (DCEZ): Summary of Current Market Research (Report).....	21 Oct 14 ✓
Sponsor Change to CG-721.....	6 Mar 15 ✓
Manufacturing Delay of Test Articles.....	19 Feb 16 ✓
Demonstration of Capabilities.....	15 Aug 16 ✓
★ DCEZ: Short-Term Field Evaluation (Report)	13 Jan 17 ✓
Go/No-Go Decision Point	6 Jul 17 ✓
Conduct Long-Term Solution Field Evaluation	31 Aug 19 ✓
★ DCEZ: Long-Term Field Evaluation (Report).....	27 Jan 20 ✓
Project End.....	27 Jan 20 ✓

★ Indicates RDC product.

Sponsor: CG-721

Stakeholder(s): CG-MSR, MSRT, AREA-3, CG-MLE

Project #: 5921	Anticipated Transition: Product Fielded Prototype
---------------------------	---

Notes:

- Leverages previous work on Project Unambiguous Warning Devices.

RDC Research Lead:
Ms. D.J. Hastings

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

Evaluation of Three-Dimensional (3D) Printing Technology for Coast Guard Applications

Mission Need: Assessment of the potential for 3D printers to improve mission readiness by reducing logistical support lead times.

Project Objectives:

- Research the advancements made with the spiral development of 3D printing technology with respect to Coast Guard applications.
- Identify CG units that are best suited to implement additive manufacturing, conduct training, and trial 3D printing technologies.
- Research cost, logistical, and performance issues that could be addressed with 3D printing and additive manufacturing.
- Work with Surface Forces Logistics Center and Aviation Logistics Center to develop the required process for approving 3D printed parts for operational use.
- Document findings and provide recommendations for decision makers.


Key Milestone / Deliverable Schedule:

Project Start.....	11 Jan 16 ✓
Identify Units for 3D Printing Trial.....	23 Feb 16 ✓
★ Evaluation of 3D Printing Technology for Coast Guard Applications (Report).....	26 Apr 17 ✓
Underway Additive Manufacturing Demonstration	29 Jun 17 ✓
★ Roadmap for Integration of Additive Manufacturing (Report)...	20 Feb 20 ✓
Project End.....	20 Feb 20 ✓

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

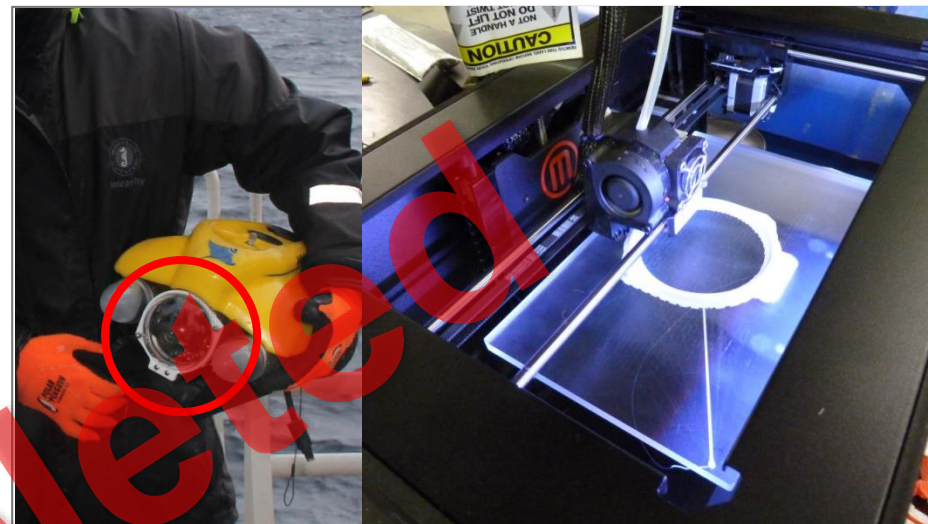

Sponsor: CG-44
Stakeholder(s): CG-11, CG-41, CG-43, CG-45, CG-731, CG-751, CG-DOL, DIUx

Project #: 7758
Anticipated Transition: Product
Fielded Prototype

Notes:

- Partnering with the Chief of Naval Operations' Rapid Innovation Cell, Naval Warfare Development Command.
- Partner with Oak Ridge and Lawrence Livermore National Labs.

RDC Research Lead:

Mr. Jason Story

CG-926 Domain Lead:

LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Safety Parameters for ICE Operations (SPICE Ops)

Mission Need: Technical data for personnel and equipment performance in extreme cold weather during ice operations.

Project Objectives:

- Establish exposure limits for Search and Rescue (SAR) team members wearing dry suits while exposed in open air.
- Evaluate the impact of extreme cold on the SAR vest and other electronic equipment to determine degradation values based on environmental conditions.
- Provide safe guidelines and identify risk mitigation strategies for personnel conducting operations on the ice.



Key Milestone / Deliverable Schedule:

Project Start.....	1 Dec 17 ✓
Conduct Human Physiological Data Collection at D9 Units.....	8 Feb 18 ✓
Develop and Acquire Electronic Equipment Test Plan	6 Jun 18 ✓
Complete Electronic Equipment Testing	21 Sep 18 ✓
Develop Personal Protective Equipment (PPE) Test Plan.....	11 Nov 18 ✓
Conduct PPE Testing	6 Dec 18 ✓
Conduct Human Modeling	15 Mar 19 ✓
★ Electronic Equipment and Dry Suit Human Modeling (Brief)...	22 Aug 19 ✓
D9 Ice Rescue Committee Facilitated Discussion	17 Oct 19 ✓
Personal Locating Beacon Testing.....	31 Jan 20 ✓
★ Safe Parameters for Ice Operations (Report)	Apr 20
Project End.....	Apr 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

Sponsor: CG-731

Stakeholder(s): CG-SAR, D1, D9, FORCECOM

Project #: 5301	Anticipated Transition: Knowledge Product Influence Tactics, Techniques, & Procedures
---------------------------	---

Notes:

- Partnering with U.S. Army Natick Soldier Research, Development & Engineering Center and U.S. Army Corps of Engineers' Cold Regions Research and Engineering Laboratory.
- Cooperative Research and Development Agreement completed for PPE testing.

RDC Research Lead:
LT Ryan Huebner

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Corrosion Control and Monitoring

Mission Need: Research and mitigate corrosion impacts on cutters by increasing mission support efficiencies and reducing costs.

Project Objectives:

- Identify and benchmark current U.S. Coast Guard (CG) corrosion mitigation strategies.
- Research the recent advancements in commercial anti-corrosion coating technologies with respect to CG surface fleet applications.
- Coordinate with U.S. Navy and other government/military services to gather their corrosion mitigation strategies.
- Stand up a CG Corrosion Integrated Product Team (IPT) to down-select promising corrosion technologies.
- Based on the research, compile a report and provide recommendations in a Corrosion Roadmap.
- Conduct Limited User Evaluations (LUE) of selected technologies.
- Research CG cutter hull blasting and recoating intervals.
- Research remote buoy corrosion monitoring systems.


Key Milestone / Deliverable Schedule:

Project Start.....	3 Oct 16 ✓
Benchmark CG Corrosion Strategies.....	15 May 17 ✓
Conduct Market Research	1 Jul 17 ✓
Review Request for Information Results.....	15 Oct 17 ✓
Review Research Results and IPT Efforts.....	8 Nov 17 ✓
★ Corrosion Control Roadmap (Report)	24 Apr 18 ✓
CGC MOHAWK Fluidized Bed Coated Watertight Doors Installed	15 Oct 18 ✓
One Component (1K) Polysiloxane Tests Begin.....	May 20
Limited User Evaluations.....	Jul 20
★ Corrosion LUE (Report).....	Sep 20
Project End.....	Sep 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

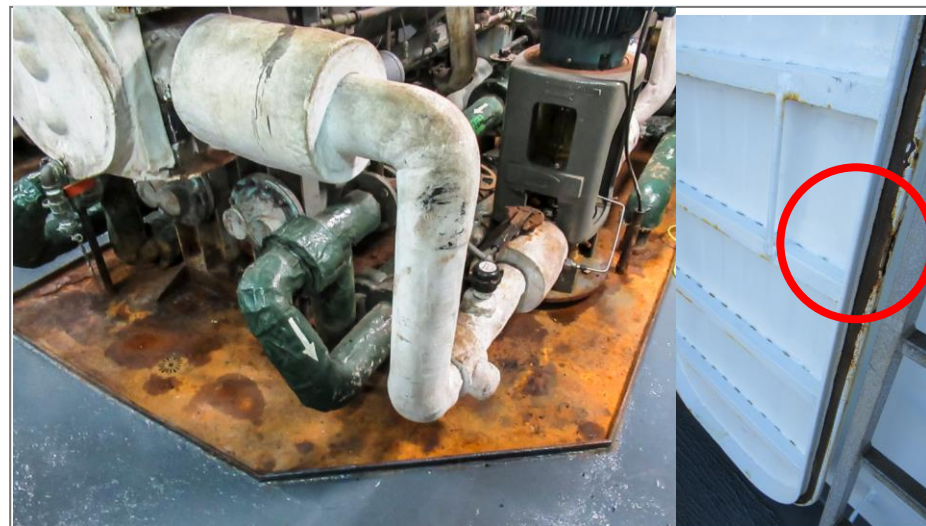

Sponsor: CG-45

Stakeholder(s): SFLC, CG-41, CG-43, CG-44, CG-751, AREA-3

Project #: 7760
Anticipated Transition: Knowledge Product
Influence Tactics, Techniques, & Procedures

Notes:

- Partnerships with the Office of Naval Research and CG Surface Forces Logistics Center (SFLC).
- Test articles scheduled for incorporation onboard 210' and 270' Medium Endurance Cutters.
- Includes Fluidized Bed Coating and One Component (1K) Polysiloxane treatments.

RDC Research Lead:

Mr. Mike Coleman

CG-926 Domain Lead:

LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Arctic Technology Evaluation 2019-2020

Mission Need: Provide support to relevant research efforts in the Arctic.

Project Objectives:

- Support projects which develop capability improvements in the execution of U.S. Coast Guard (CG) missions in the Arctic.
- Nurture joint efforts and interagency cooperation between government sectors and civilian entities on the North Slope and abroad.
- Facilitate and support other Arctic projects, including Department of Homeland Security Science and Technology Directorate initiatives.
- Monitor technology progression.

Key Milestone / Deliverable Schedule:

Project Start.....	3 Dec 18	✓
Identify Partners/Technologies/Test Plans (FY19)	14 Jun 19	✓
Solicit FY20 Research Efforts/Partners	30 Aug 19	✓
Conduct Tests/Demonstrations on USCGC HEALY (FY19)	28 Oct 19	✓
★ Communications Technology in the Arctic (Application Note).....	Apr 20	
Identify Partners/Technologies/Test Plans (FY20)	Jun 20	
Solicit FY21 Research Efforts/Partners	Jul 20	
Conduct Tests/Demonstrations on USCGC HEALY (FY20)	Sep 20	
★ Arctic Technology Evaluation FY20 (Application Note).....	Dec 20	
Project End.....	Dec 20	

★ Indicates RDC product.




Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

47

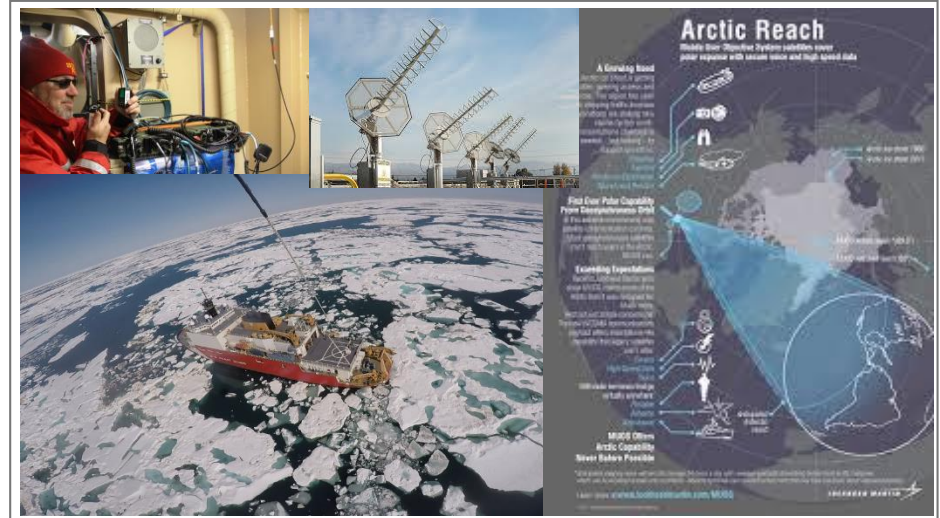

Sponsor: CG-751

Stakeholder(s): D17, PAC-5, LANT-5

Project #: 62102	Anticipated Transition: Knowledge Product Future Technology
-------------------------	---

Notes:

- Outreach partners include the Bureau of Safety and Environmental Enforcement, the Arctic Domain Awareness Center, Department of Defense Labs, U.S. Northern Command, and National Labs.

RDC Research Lead:
Mr. Scot Tripp

CG-926 Domain Lead:
Ms. Holly Wendelin

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Bromine-Free Water Purification System

Mission Need: Evaluate newer, less hazardous water purification systems.

Project Objectives:

- Install and operate a Bromine-Free Water Purification System (BF-WPS) onboard a U.S. Coast Guard (CG) National Security Cutter based on system advances made by the U.S. Navy.
- Explore potential issues/aspects of transitioning use of BF-WPS to new CG cutters:
 - Identify feasibility of incorporating BF-WPS on various cutter classes.
 - Estimate ownership costs to include procurement, installation/retrofit, operation, and maintenance.
 - Identify potential benefits of utilizing BF-WPS on CG cutters.

Key Milestone / Deliverable Schedule:

Project Start..... 27 Jul 19 ✓

BF-WPS Purchase and Begin 3-Month Pilot Study..... May 20

★ **Bromine-Free Water Purification System (Brief)..... Jun 20**

Conclude BF-WPS Pilot Feasibility Analysis..... Feb 21

★ **Bromine-Free Water Purification System Pilot Study (Report).....Mar 21**

Project End..... Mar 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor: Surface Force Logistics Center (SFLC)

Stakeholder(s): CG-45, SFLC-LRE

Project #: 5507	Anticipated Transition: Pending Acquisition	Product
---------------------------	---	----------------

Notes:

- Legislative requirement.

RDC Research Lead:
Ms. D. J. Hastings

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Low-Cost MDA Pilot


Mission Need: Improve Maritime Domain Awareness (MDA) in remote areas.

Project Objectives:

- Conduct a pilot study/assessment to determine the efficacy of using low-cost commercially available unmanned surface systems, in combination with or on existing fleet platforms, to enhance maritime domain awareness.
- Test technology solutions used by small, remote Pacific Island states and other technologies with little or no logistics funding.
- Utilize industry engagement and technology demonstrations, focus on contractor owned and operated technology.

Key Milestone / Deliverable Schedule:

Project Start.....	6 Jun 18 ✓
Issue Request for Information for Industry Engagement.....	30 Sep 18 ✓
Issue Request for Proposal for Industry Owned and Operated Solutions.....	7 Nov 19 ✓
Award Contract(s).....	7 Feb 20 ✓
★ Low-Cost Maritime Domain Awareness Demonstration Plan (Brief).....	May 20
Field Demonstration Complete.....	Aug 20
★ Low-Cost Maritime Domain Awareness Pilot Study (Report).....	Apr 21
Project End.....	Apr 21

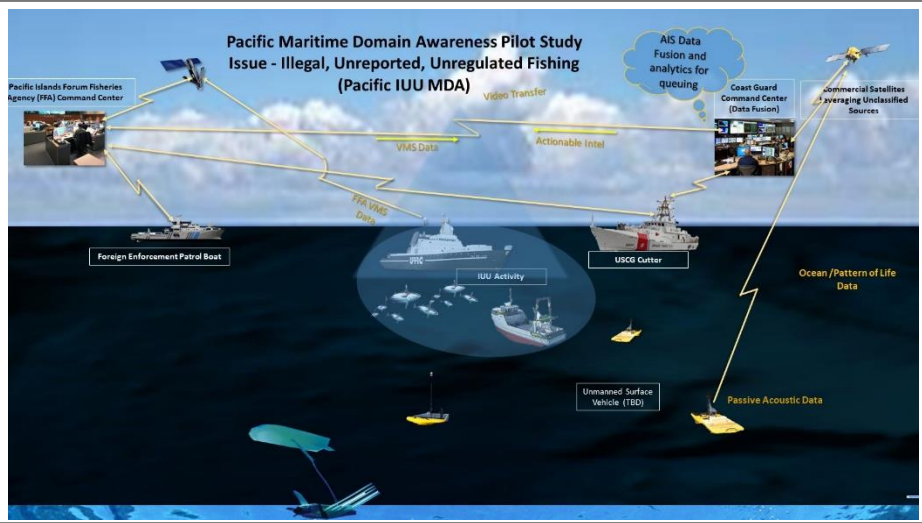

Sponsor:	CG-26
Stakeholder(s):	CG-711, CG-721, CG-761, CG-MLE, LANTAREA, D14, PACAREA, D17
Project #:	Anticipated Transition: Knowledge Product
7210	Future Technology
Notes: <ul style="list-style-type: none">• Legislative requirement.• Include the U.S. Coast Guard (CG) Auxiliary if applicable.	
RDC Research Lead: Mr. Scot Tripp	CG-926 Domain Lead: Mr. Scott Craig
For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil	

★ Indicates RDC product.

Counter Unmanned Underwater Vehicle (C-UUV)/Anti-Swimmer Technology

Mission Need: Improved detection, tracking, classification, and deterrence of underwater threats to U.S. Coast Guard (CG) assets.

Project Objectives:

- Phase I – Summarize currently available high technology readiness level c-UUV and anti-swimmer technologies that can be demonstrated for CG use cases.
- Phase II – Conduct a limited user evaluation to identify baseline and desired functional characteristics.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 18 ✓
C-UUV/Anti-Swimmer Technology (Brief).....	Jun 20
Limited User Evaluation.....	Jan 21
★ C-UUV/Anti-Swimmer Limited User Evaluation (Report)	Jul 21
Project End.....	Jul 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

50



Sponsor: CG-721

Stakeholder(s): CG-45, CG-731, CG-761, AREA-3

Project #: 5922	Anticipated Transition: Knowledge Product Future Technology
---------------------------	---

Notes:

- Build on past RDC anti-swimmer work.
- Coordinate with other government agencies.
- Possible Cooperative Research & Development Agreements for limited user evaluation.

RDC Research Lead:
Mr. Mike Coleman

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Drug and Explosives Detection Technologies

Mission Need: Improved efficiency in multiple agent detection with accuracy and reliability required to support legal prosecution.

Project Objectives:

- Provide more effective and efficient drug and explosive detection capability options for use by U.S. Coast Guard (CG) members during maritime and shore-based missions.
- Provide support to plan, execute, and report results from Handheld Illicit Drug – Explosive Trace Detector (HID-ETD) Limited User Evaluation (LUE) as part of the U.S. Department of Homeland Security's (DHS) Science and Technology Directorate (S&T) Strategic Sourcing Initiative.

Key Milestone / Deliverable Schedule:

Project Start.....	1 Oct 19 ✓
HIT-ETD Technical Evaluation CG Feedback Submitted.....	Apr 20
Begin DHS System Assessment and Validation for Emergency Responders (SAVER) Program	May 20
★ Drug and Explosives Detection SAVER (Report).....	Jul 20
HID-ETD LUE Plan Developed and Devices Obtained.....	Jan 21
Distribute Devices and Begin HID-ETD LUE.....	Feb 21
Complete HIT-ETD LUE and Retrieve Devices.....	Jul 21
★ Handheld Illicit Drug – Explosives Trace Detector (Report).....	Sep 21
Project End.....	Sep 21

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center



Sponsor:	CG-721
Stakeholder(s):	DSF, NSF, CG-MLE, DHS S&T, CG-1B3, FORCECOM
Project #:	Anticipated Transition: Knowledge Product
5807	Influence Tactics, Techniques, & Procedures
Notes: <ul style="list-style-type: none"> • Partnerships: Countering Weapons of Mass Destruction Office, U.S. Secret Service, Federal Protective Services, National Urban Security Technology Laboratory, Transportation Security Laboratory, Federal Emergency Management Agency, Transportation Security Administration, and U.S. Customs and Border Protection. • Leverages past RDC Project 5802, Maritime Trace Narcotic Identification/Verification. 	
RDC Research Lead:	CG-926 Domain Lead:
Ms. D.J. Hastings	LT Steve Hager
<i>For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil</i>	

Operational Test Agent (OTA) for the sUAS for NSC Program

Mission Need: Independent and objective evaluation of Small Unmanned Aerial Systems (sUAS) operational suitability and effectiveness.

Project Objectives:

- Generate sUAS test plan for the National Security Cutter (NSC) Program.
- Perform Operational Testing & Evaluation (OT&E) of sUAS.
- Provide OT&E report to the sponsor program office.

Key Milestone / Deliverable Schedule:

Project Start.....	27 Jun 18 ✓
Develop Test Plan.....	2 Apr 19 ✓
Conduct OT&E.....	19 Nov 19 ✓
Summary Report of OT&E	16 Dec 19 ✓
★ OTA for the sUAS for NSC Program (Report).....	11 Feb 20 ✓
Project End.....	11 Feb 20 ✓

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

52



Sponsor: CG-931

Stakeholder(s): CG-711

Project #: 7702
Anticipated Transition: Knowledge Product
Acquisition Milestone Support

Notes:

- Direct support to Procurement, Construction, and Improvement.

RDC Research Lead:
LTJG Ryan Major

CG-926 Domain Lead:
Mr. Scott Craig

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Diesel Outboard Development

Mission Need: Single fueled fleet.

Project Objectives:

- Research current developmental stage of diesel outboards applicable to U.S. Coast Guard (CG) usage.
- Conduct cost-benefit analysis of implementing diesel outboard engines in the CG.
- Investigate partnership options with manufacturers and other government agencies and test promising diesel outboard engine technologies to better understand performance capabilities.
- Provide recommendations for potential future acquisition initiatives, as appropriate.

Key Milestone / Deliverable Schedule:

Project Start.....	27 Feb 14 ✓
Issue Request for Information.....	3 Apr 14 ✓
★ Diesel Outboard Engine Market Survey Results (Brief).....	8 Sep 14 ✓
★ Diesel Outboard Engine Cost-Benefit Analysis (Report).....	24 Jul 15 ✓
Key Decision Point: Determine Path Forward.....	24 Jul 15 ✓
Conduct Spark-Ignited Diesel Outboard Engine Testing.....	31 May 17 ✓
Conduct Compression-Ignited Diesel Outboard Engine Testing.....	16 Nov 18 ✓
Key Decision Point: Cancel High Compression-Ignition Engine Testing.....	11 Jun 19 ✓
★ Diesel Outboard Engine Feasibility (Report).....	Apr 20
Project End.....	Apr 20

★ Indicates RDC product.




Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

53

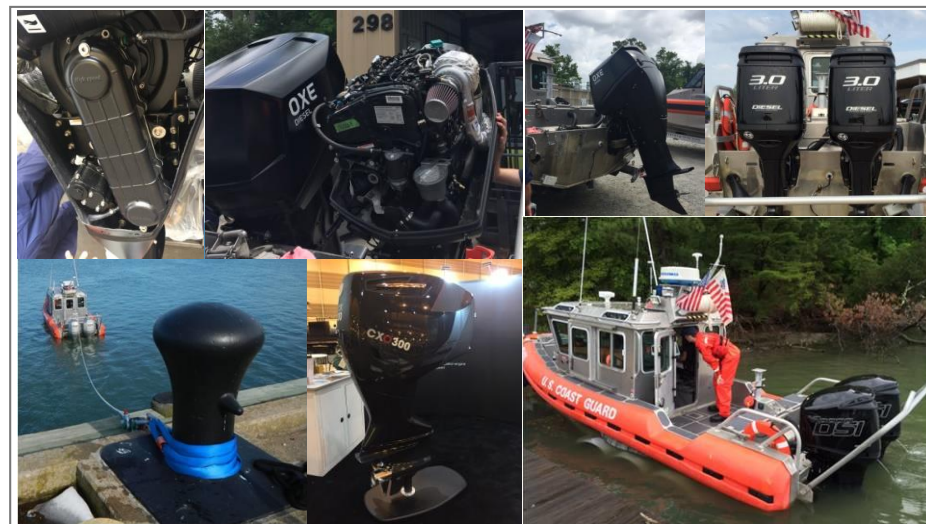

Sponsor: CG-731

Stakeholder(s): CG-46, CG-451

Project #: 4110	Anticipated Transition: Knowledge Product Acquisition Milestone Support
---------------------------	---

Notes:

- Project includes Cooperative Research and Development Agreements.
- Establish partnerships with Joint Task Force-East, U.S. Customs and Border Protection, U.S. Immigration and Customs Enforcement, and U.S. Department of Homeland Security Science and Technology Directorate.
- Continue to leverage partnerships with the U.S. Navy Combatant Craft Division to test diesel outboard engines.

RDC Research Lead:

Mr. Jason Story

CG-926 Domain Lead:

LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

Support of Alternatives Analysis for the Waterways Commerce Cutter

Mission Need: Support replacing the outdated fleet of inland cutters.

Project Objectives:

- Support Sponsor's Integrated Project Team tasked to:
 - Identify replacement options for the inland fleet.
 - Review new design options for replacement hulls.
 - Review the cost and consequences of buying, leasing, or contracting other boats to perform similar missions.
- Support drafting the Alternatives Analysis Study Plan (AASP) for the Waterways Commerce Cutter.
- Support execution of the AASP by the Naval Sea Systems Command (NAVSEA).

Key Milestone / Deliverable Schedule:

Project Start..... 1 Jun 17 ✓

★ **Waterways Commerce Cutter Alternatives Analysis Study Plan (AASP)..... 2 Oct 18 ✓**

AASP Liaison Support to NAVSEA..... Apr 20

★ **Support of Alternatives Analysis for the Waterways Commerce Cutter (Closeout Memo)..... Apr 20**

Project End..... Apr 20

★ Indicates RDC product.



Acquisition Directorate
Research & Development Center

UNCLAS/USCG Research & Development Center
Internet Release is Authorized

April 2020
Version date

54



Sponsor: CG-932

Stakeholder(s): CG-751, LANT-5, D8

Project #: 6812	Anticipated Transition: Knowledge Product Acquisition Milestone Support
---------------------------	---

Notes:

- Direct support to Procurement, Construction, and Improvement.
- Leverage all previous approved and signed Acquisition documents.

RDC Research Lead:
LTJG Ryan Major

CG-926 Domain Lead:
LT Steve Hager

*For more information, call (860) 271-2600 or
e-mail RDC-Info@uscg.mil*

FY20 Science & Technology Innovation Center (CG-STIC) Tasks

Purpose: To establish a collaborative relationship between the U.S. Coast Guard Innovation Center and the Department of Homeland Security Science and Technology Directorate to share and advance technologies that will be mutually beneficial to both parties.

Title	Objective	Office Supported	Funding Type	RDC POC	CG-926 Domain Lead	Due/Delivery Date
Human Language Technology (HLT)	<i>Examine HLT and investigate previously unknown or untried techniques for operational use.</i>	CG-2 CG-721 CG-731	DHS S&T	LCDR Anderson Ogg	CDR James Small	31 Dec 19 ✓
Transducer Puller for Bay Class	<i>Examine a transducer puller to aid in the removal of hull-mounted transducers in a way that makes the process more efficient, reduces risk to the personnel removing the transducer, and reduces risk of damaging the hull seal making for safer and more efficient replacement.</i>	CG-45 SFLC	DHS S&T	LTJG Ryan Major	CDR James Small	27 Jan 20 ✓
Handheld X-ray Backscatter Technology	<i>Examine handheld X-ray backscatter technology and investigate previously unknown or untried techniques for operational use.</i>	CG-2 CG-721 CG-731	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Jun 20
K9 Equipment Limited User Evaluation	<i>Examine life-saving solutions for K9 companions to include K9 helmets with integrated hearing and eye protection and multi-purpose ballistic and hoist vests.</i>	CG-5R	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Jun 20
Hydronalix Remotely Piloted Vessel	<i>Test the capabilities of lifesaving rescue robots technology and investigate previously unknown or untried techniques for operational use.</i>	CG-SAR DOL-3	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Jun 20
Mobile Tethered Video Systems	<i>Examine mobile tethered video systems and investigate previously unknown or untried techniques for operational use.</i>	CG-7 DCMS CG-5R	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Jul 20
Maritime Object Tracking Technology (MOTT) 1.75	<i>Finalize design as needed from drop testing, obtain ACCB clearance, and test/evaluate for operational use.</i>	CG-711 CG-721 CG-731	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Jul 20
Teleoperated RBS Proof Of Concept	<i>Summary of background information, test results, and conclusions relating to the teleoperated RBS proof of concept demonstration.</i>	CG-731	DHS S&T	LTJG Ryan Major	Ms. Minh-Thu Phan	Sep 20

For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil.



FY20 Short Term Analytical Support Efforts

Purpose: Provide short term analytical support to CG decision makers with a means to access quick, inexpensive analyses to investigate a wide range of technology issues relating to current or planned CG operations or procurements. Larger analytical support projects will typically require funding to cover the cost of RDC labor & overhead and other direct costs.

Branch	Title	Objective	Office Supported	RDC POC	CG-926 Domain Lead	Due/Delivery Date
Aviation	REACT Report: ESS Geo-Position Accuracy	<i>The report will present conclusions concerning ESS geo-positioning accuracy as a function of calibration and maintenance actions performed and recommended re-calibration requirements.</i>	ALC ESD RW Air Stations CG-41 CG-711	Mr. Sean Lester	Mr. Scott Craig	13 Feb 20 ✓
Aviation	REACT Report: Rotary-wing Trail Lines	<i>A short, summary report of previous analysis completed by RDC on the use of gloves and trail lines during hoisting evolutions.</i>	CG-711	Mr. Sean Lester	Mr. Scott Craig	Jun 20
Surface	REACT Report: Rough Bar Illumination	<i>Identify low weight and low power lighting and how this lighting can be installed onto the MLB platform to increase situational awareness during surf operations and rough bar escorts. The lights will enable crews to see the incoming waves and allow escorted vessels to better see the MLB to safely follow it through the rough bar conditions. Also investigate land based lighting and improved flares to illuminate rough bars.</i>	CG-731 to support Coast Guard 47' MLB fleet	Mr. Brian Dolph	LT Steve Hager	Jul 20
C5I	REACT Report: LED Test Results	<i>The test results report of radiated emission from LED assemblies will be used to determine updates to regulations for placement of lighting fixtures on vessels, and guidance for manufactures of the assemblies.</i>	CG-672	Mr. Ross Vassallo	Ms. Holly Wendelin	Sep 20

For more information, call (860) 271-2600 or e-mail RDC-Info@uscg.mil.

